





Week 1 to 3

-  Avanti unit installed
-  Hoarding Adjusted
-  New Gates installed
-  Main compound formed
-  WDC Staff and Visitor parking areas designated

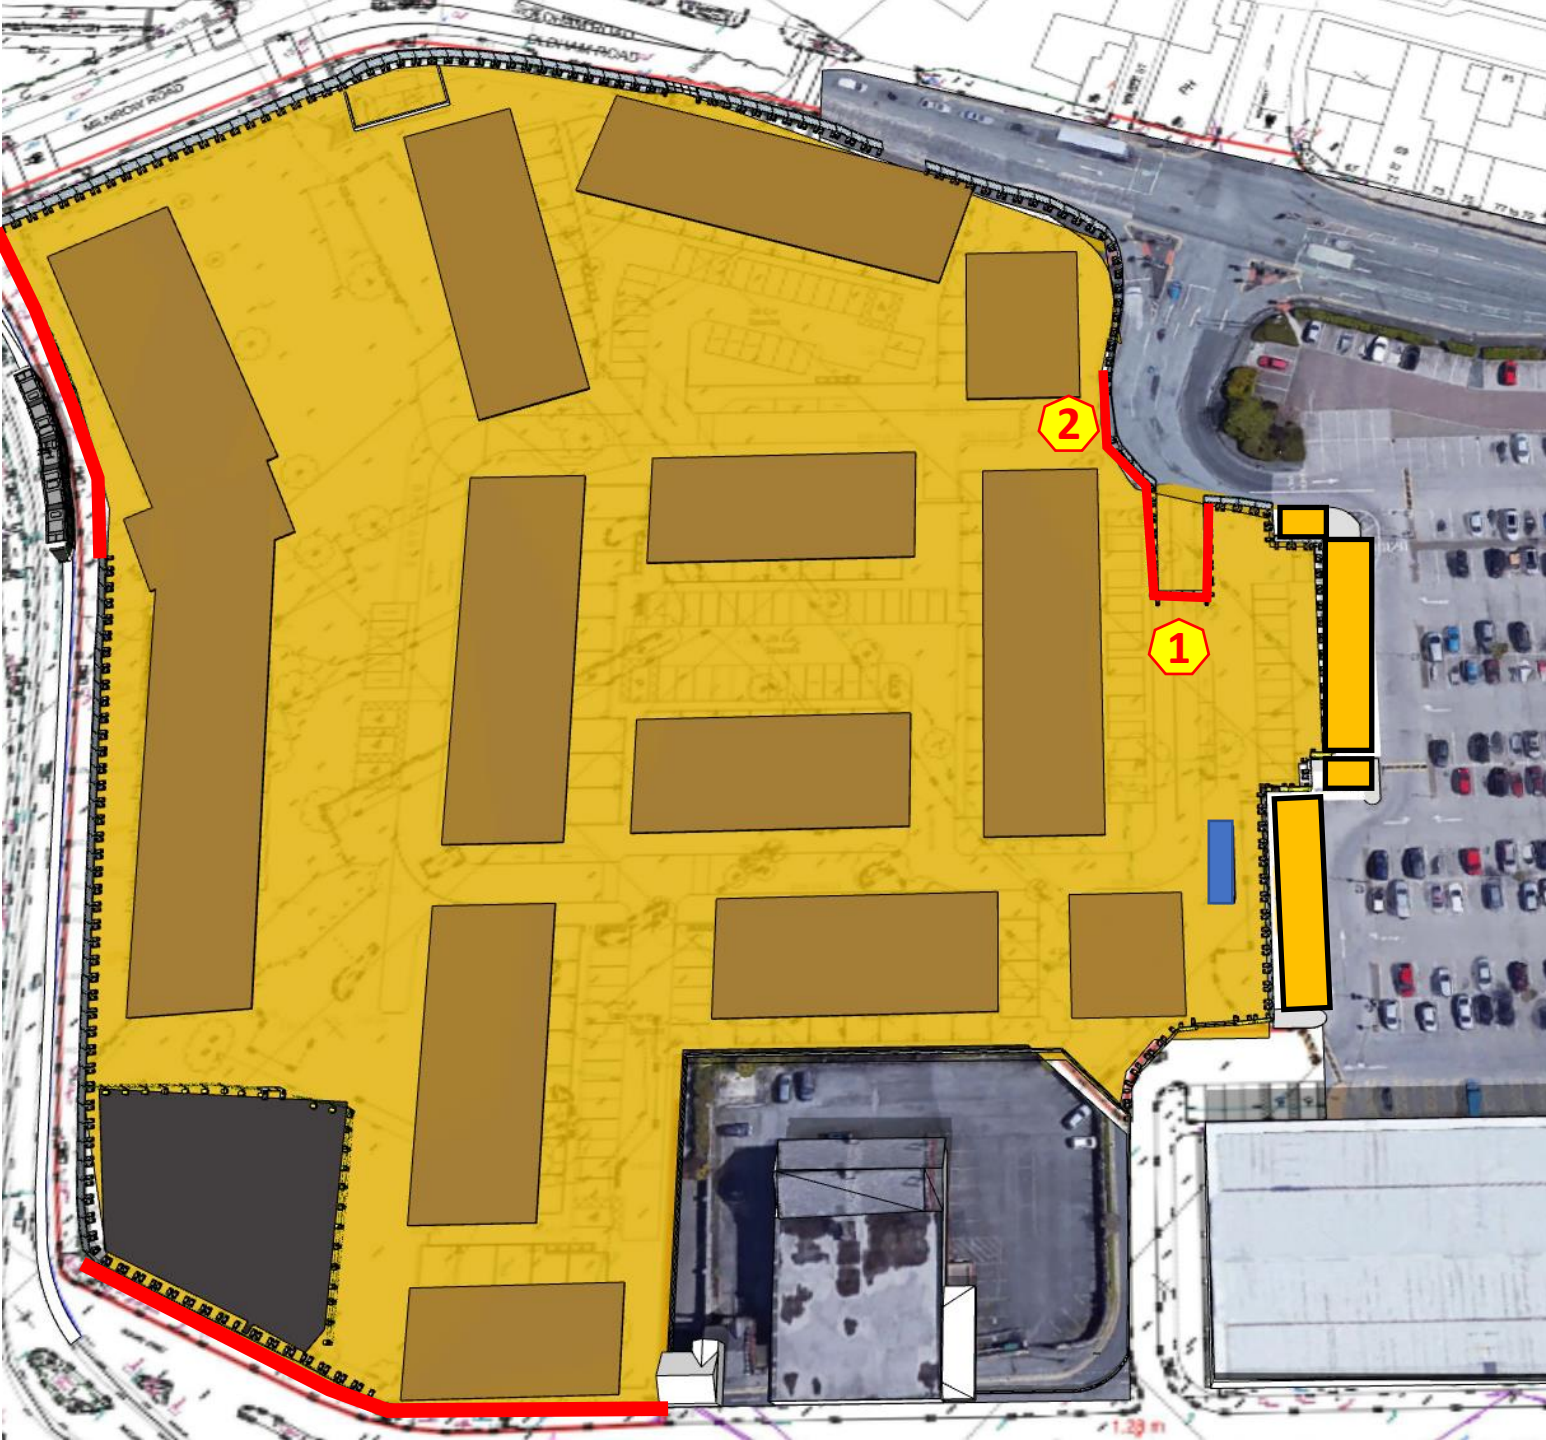


**Station Gardens
Rochdale**

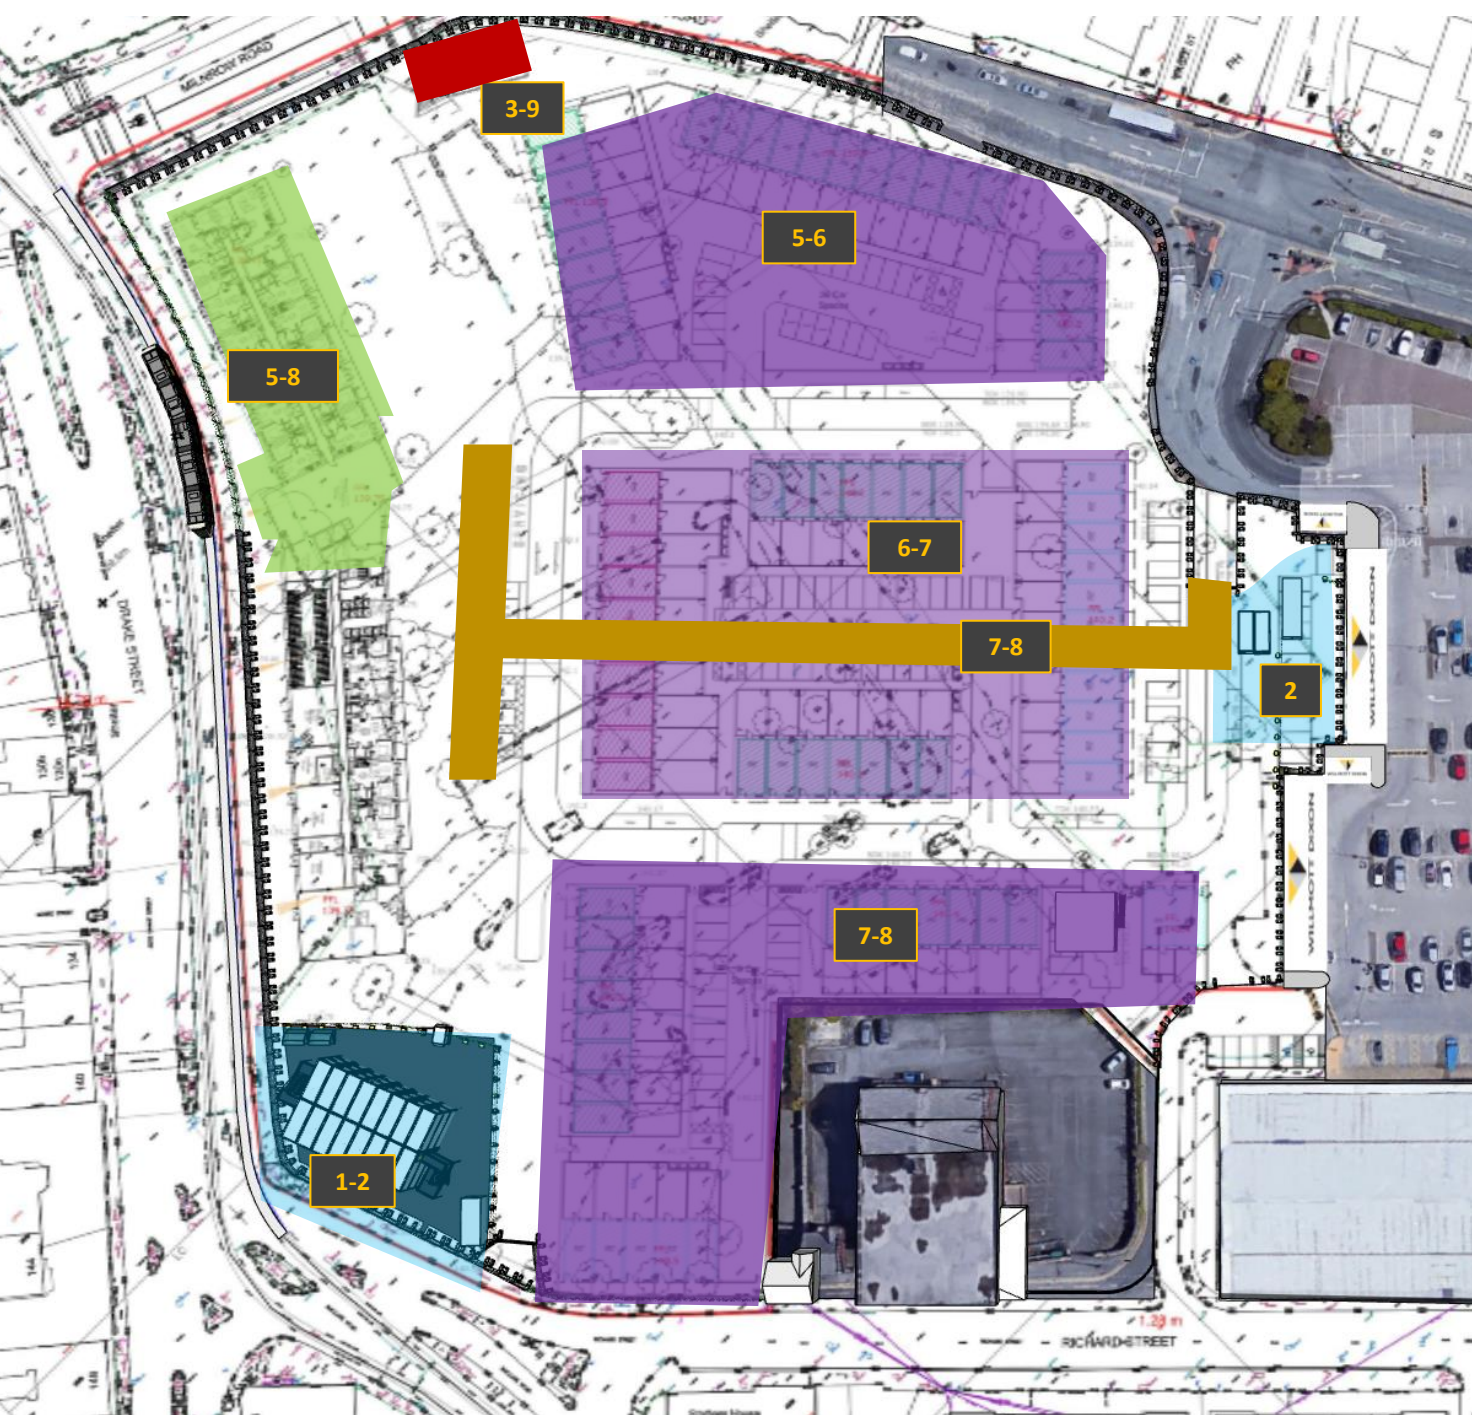


Week 3 to 8


-  Main accommodation and gatehouse established
-  Substation Retaining wall
-  PCC Piles North Wing
-  Vibro Piles
-  Main Drainage Connection
-  Haul road/road plates across Block F+D

Project Week Number

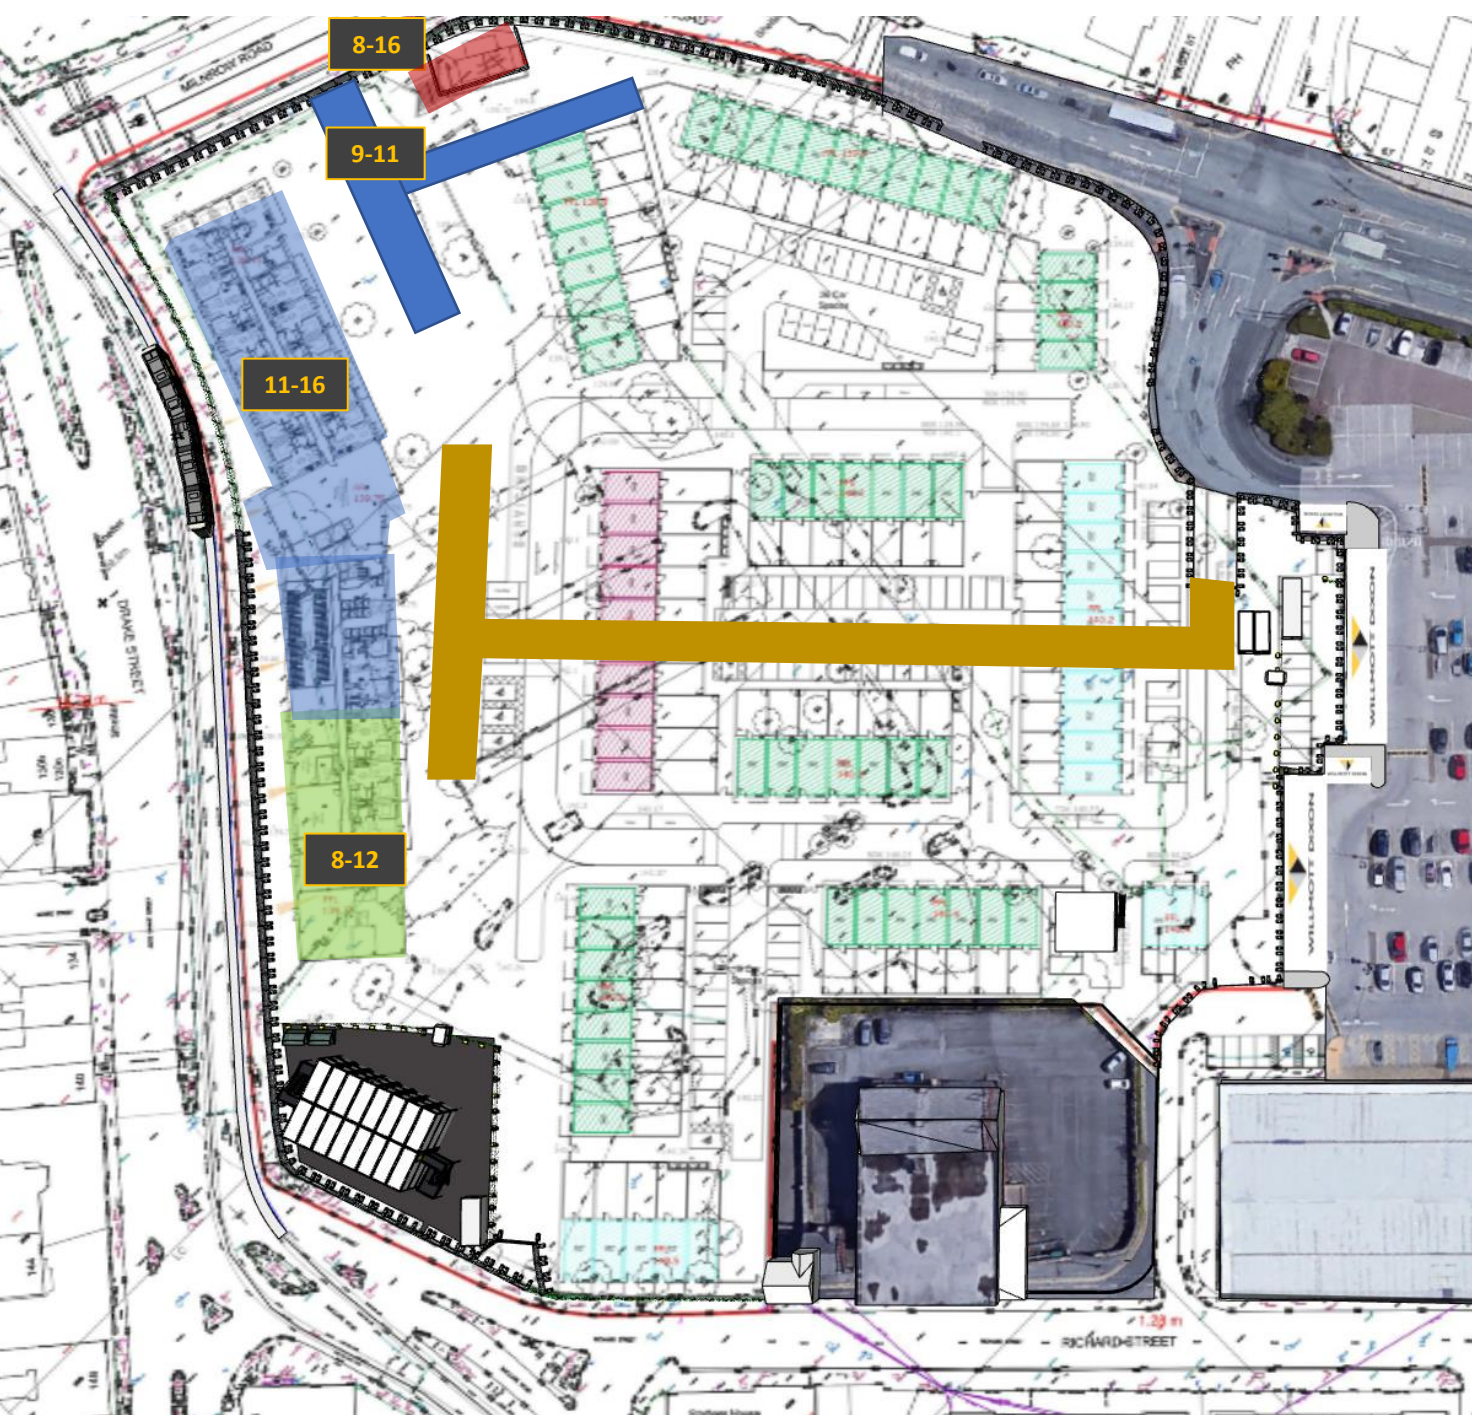


Week 8-16

-  Substation Housing
-  PCC Piles South Wing
-  Main Drainage works
-  Apartment Substructure

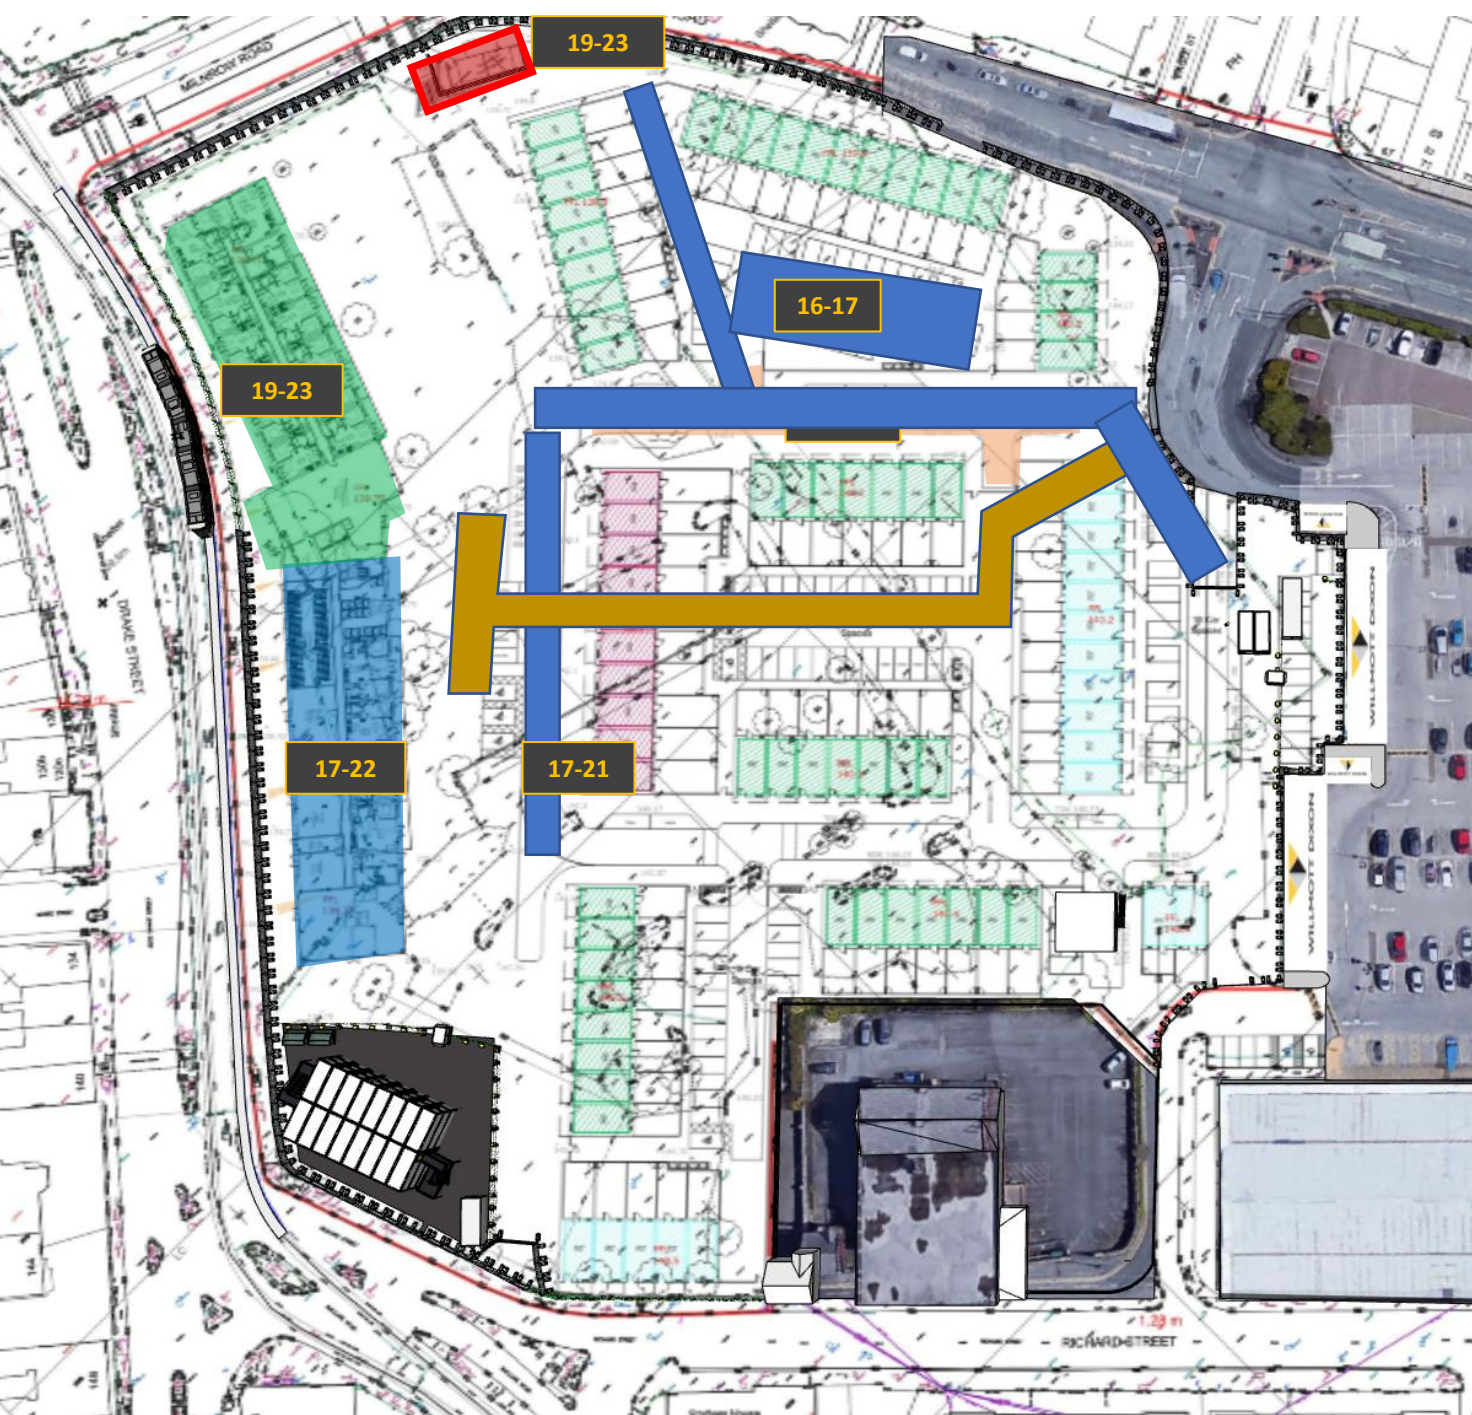

Week 16-23

-  Apartment Substructure
-  Apartment Slabs
-  Substation Fitout
-  Main Drainage works
-  New Road to base coat
-  House Substructure

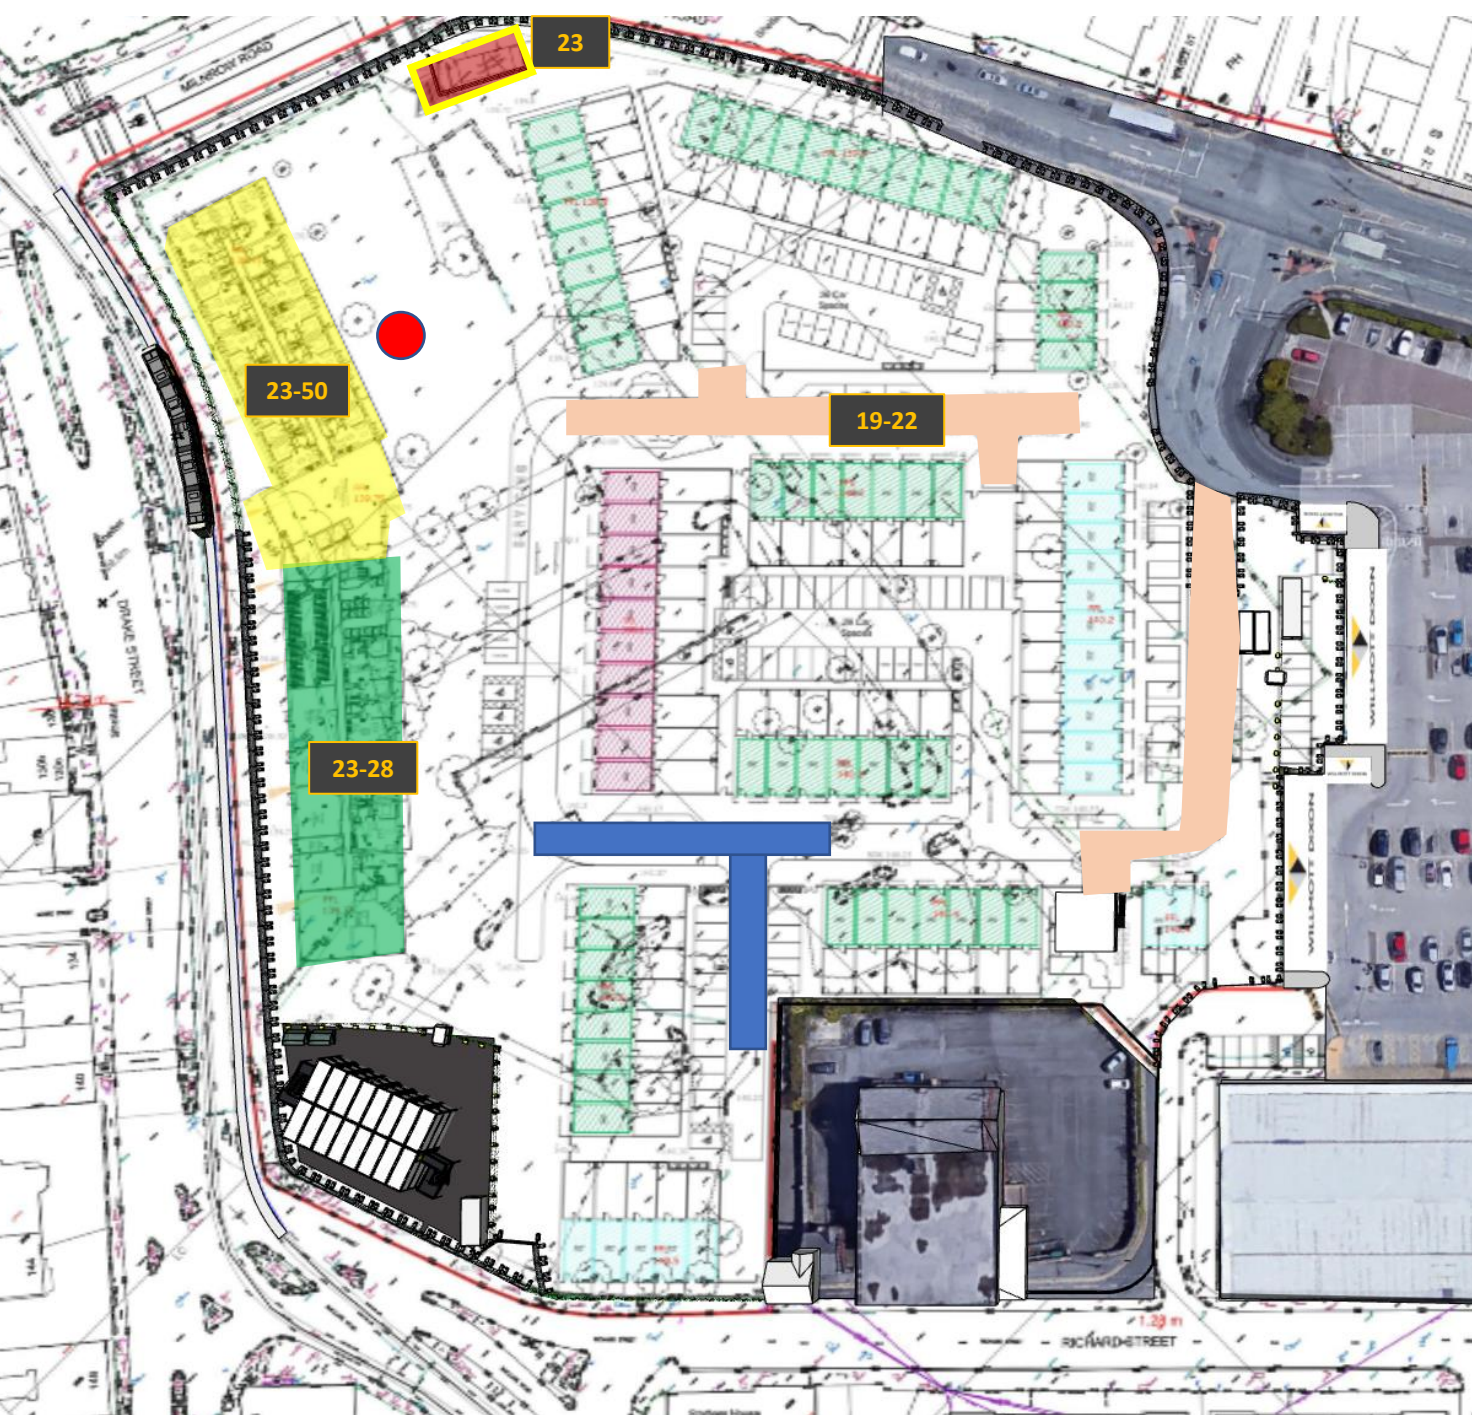

Week 23-28

- Apartment Slabs
- Power on week 23 *
- Main Drainage works
- New Road to base coat
- House Foundations
- Tower Crane – instal week 24
- RC Frame

* Week 23 power on dependent upon supplier and substation order made ahead of contract award


New Road to base coat


House Substructure

Tower Crane – South installed wk 28

RC Frame


Houses Shell [gang No.]

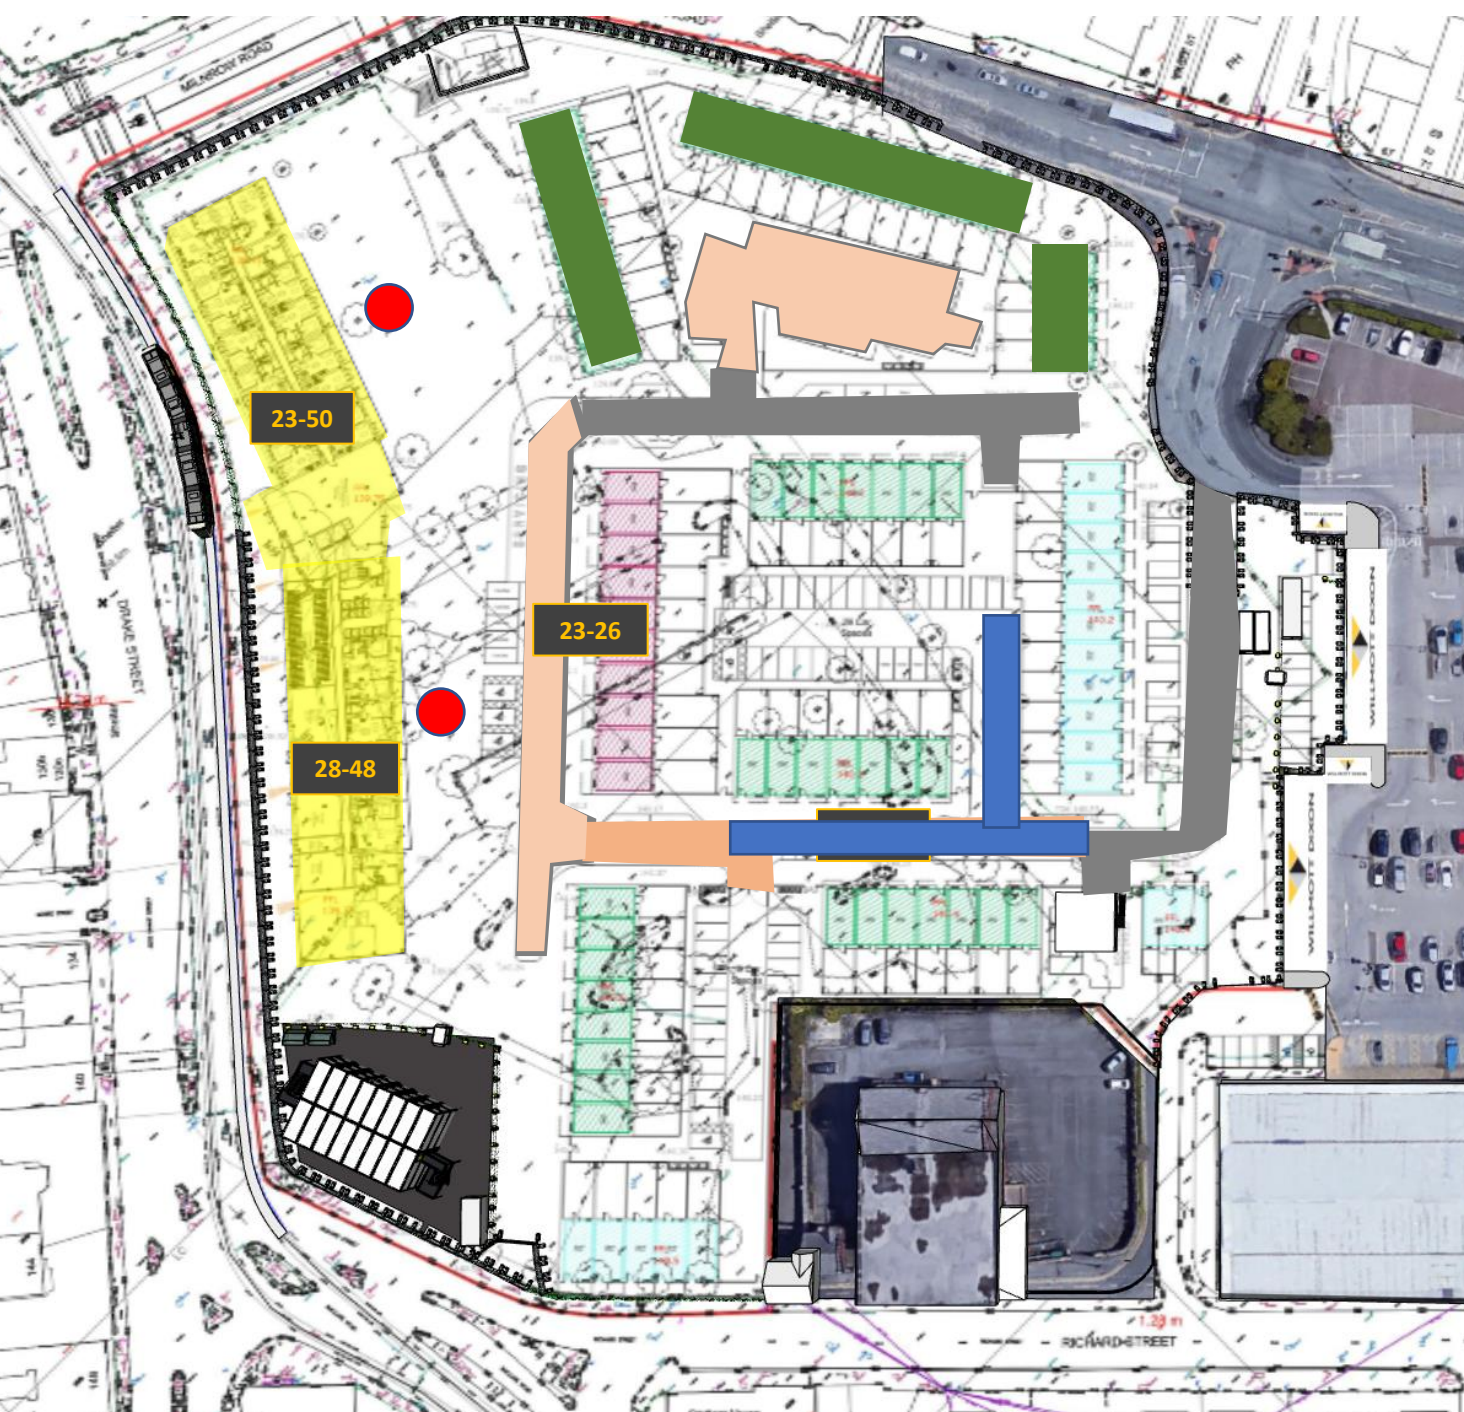

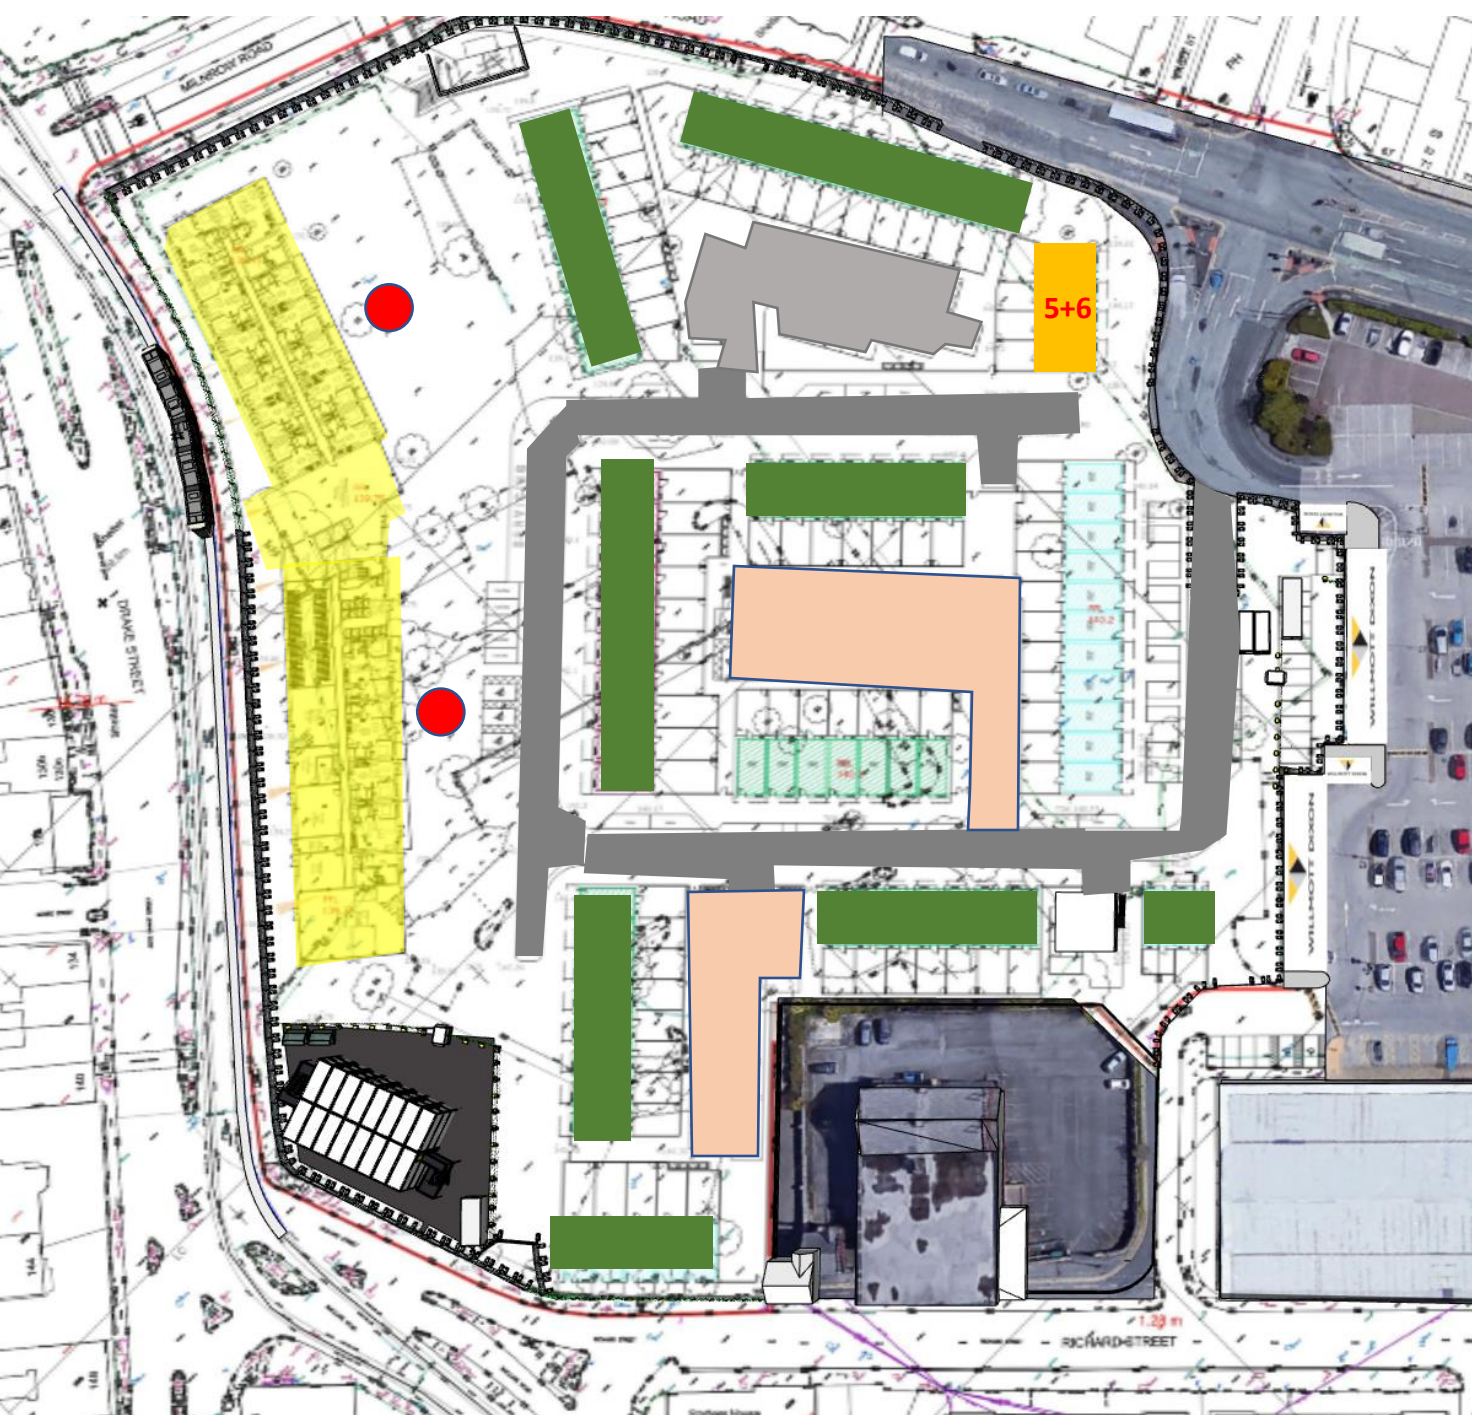

Week 30

-  New Base Coat
-  House Substructure
-  RC Frame
-  Houses Shell [gang No.]
-  Tower crane

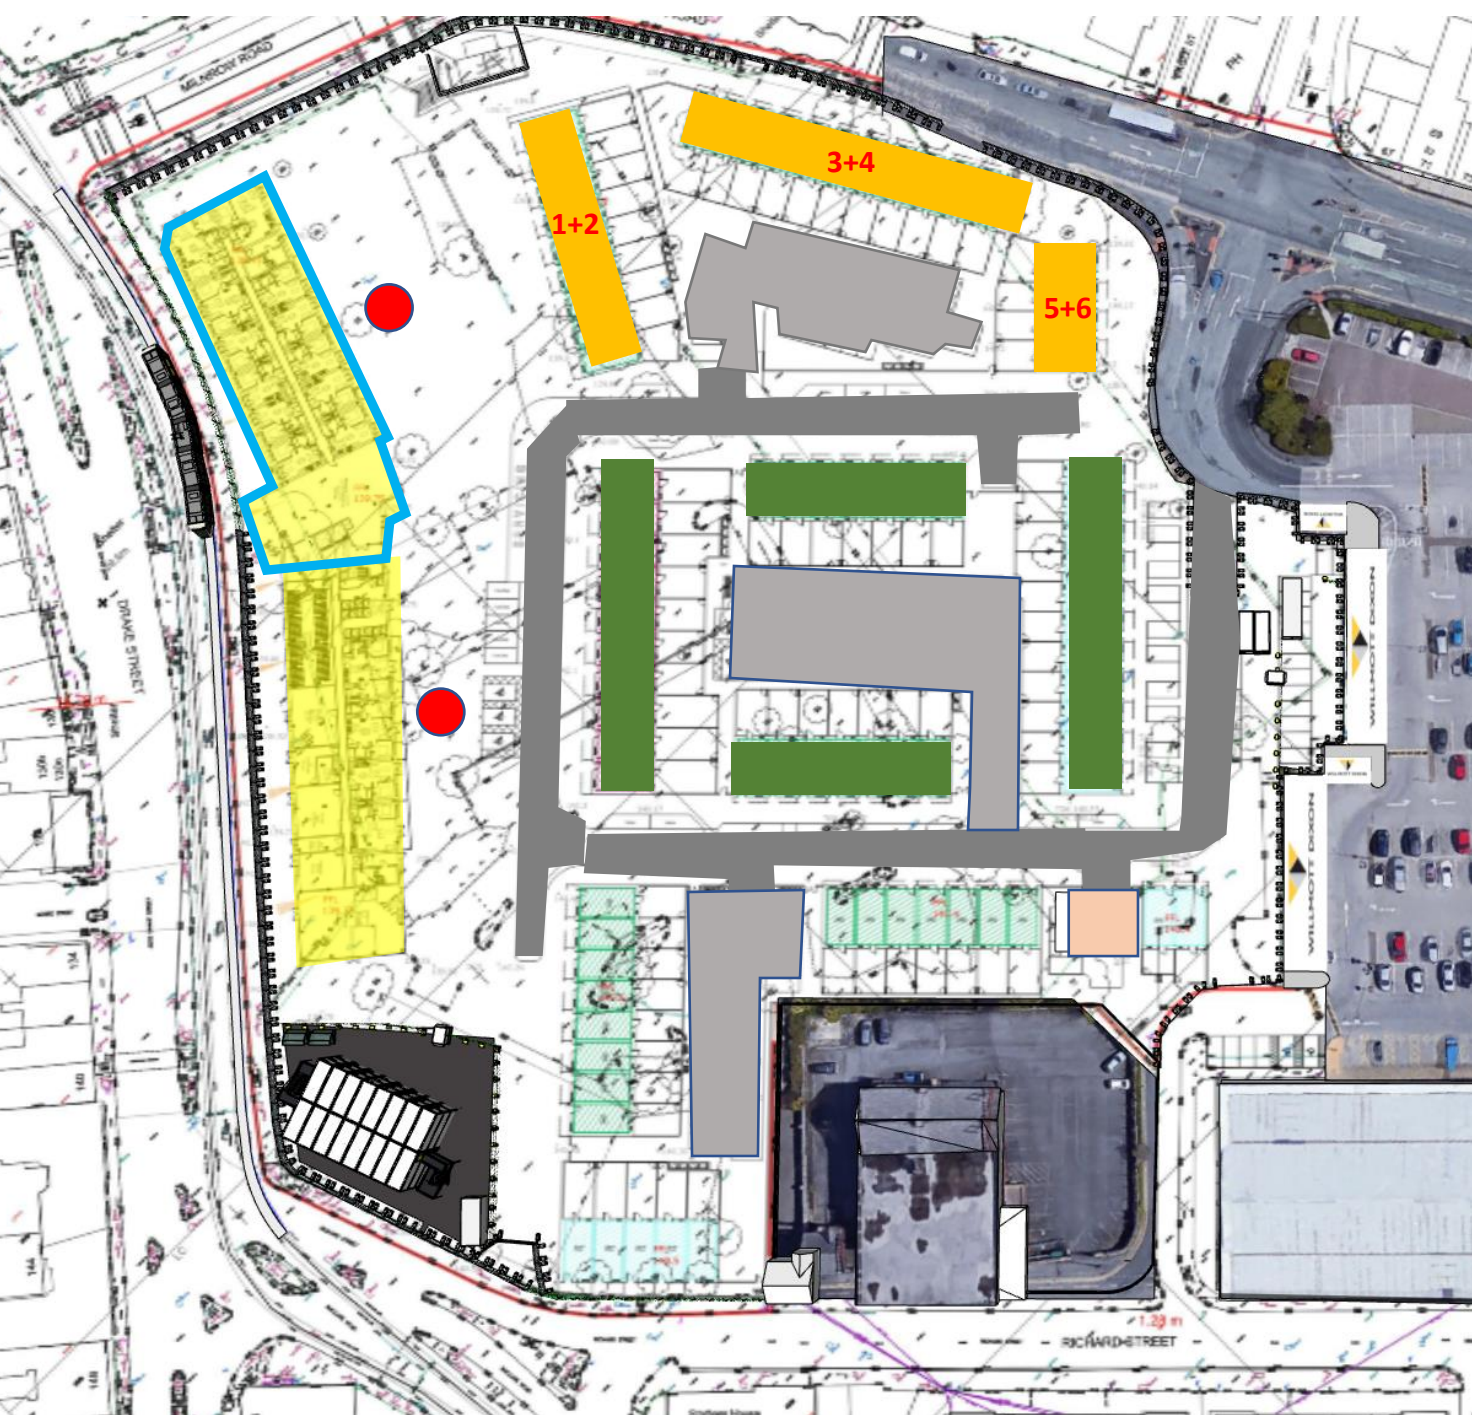


Week 30-43




Station Gardens
Rochdale

- New Road to base coat
- House Substructure
- RC Frame
- Houses Shell [gang No.]
- Apartment SFS/Windows

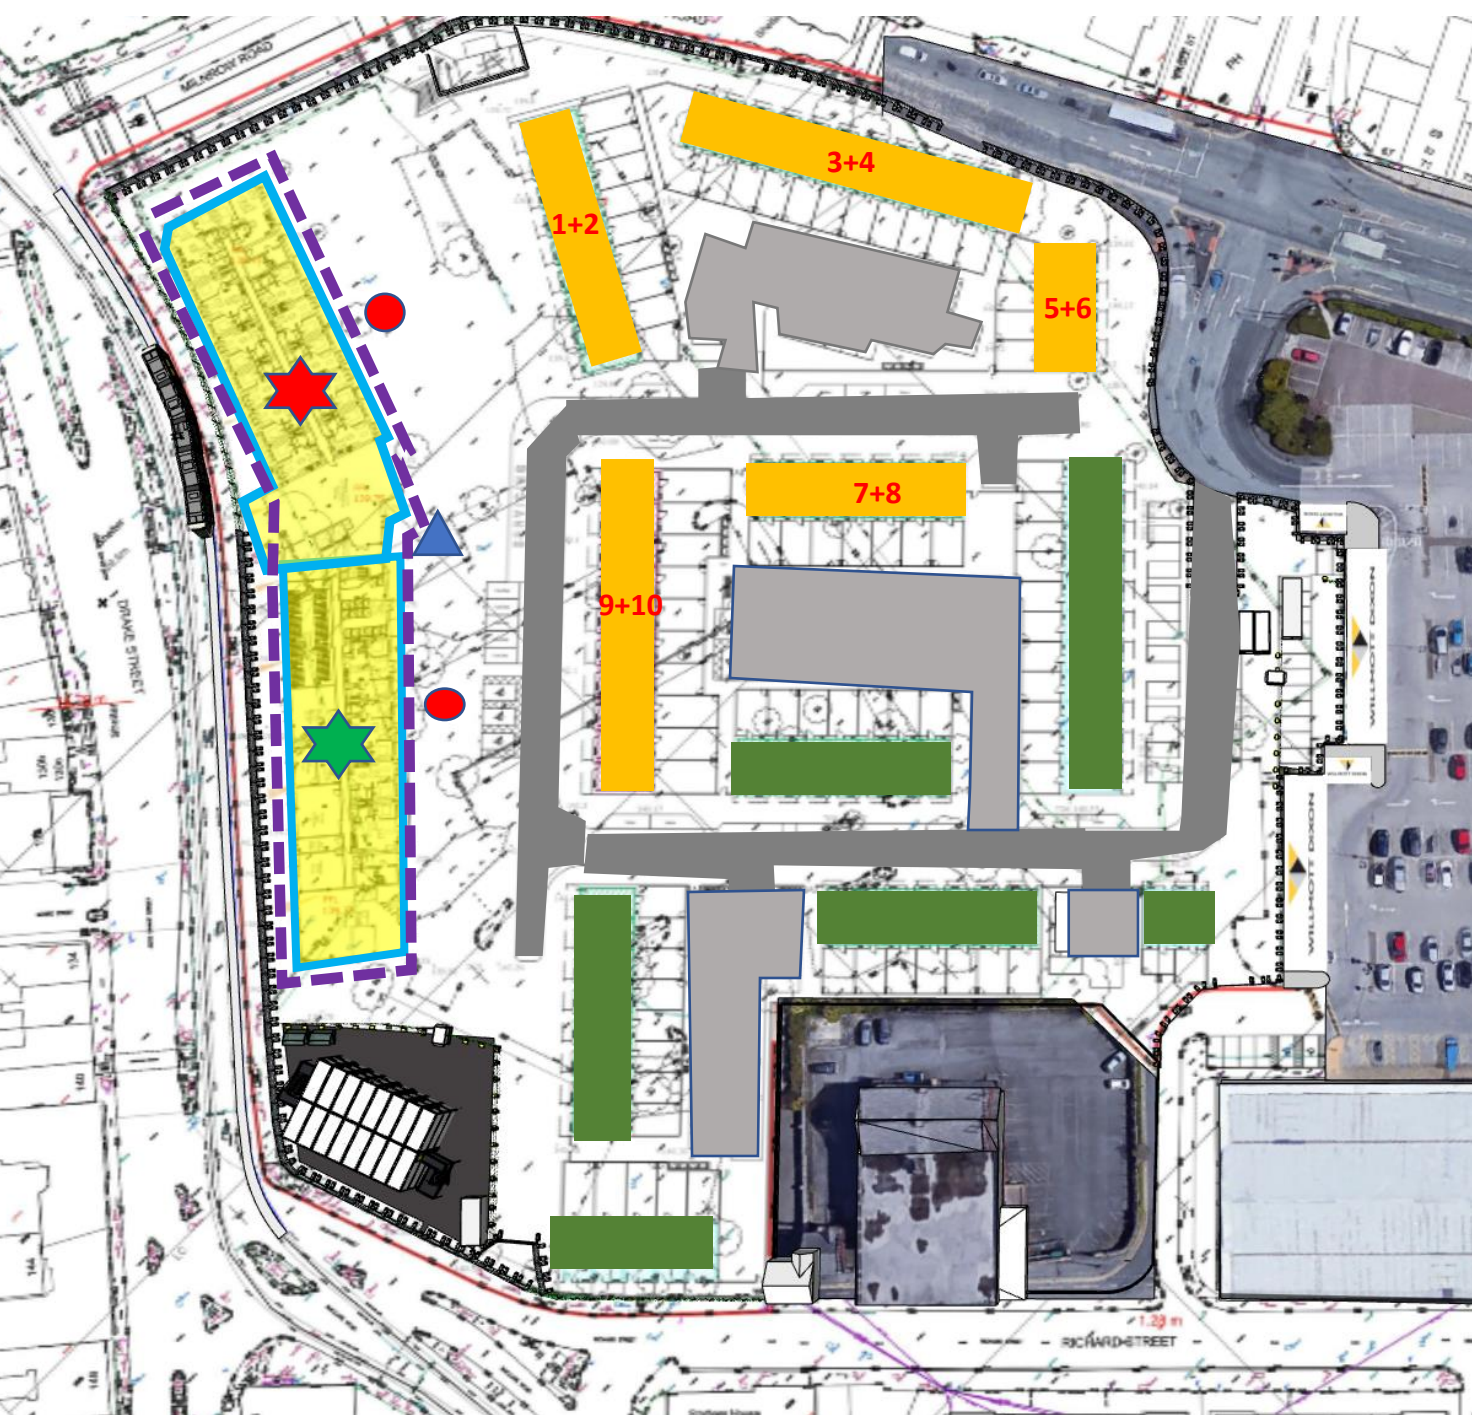


Week 43-47

-  House Substructure
-  RC Frame [pods positioned]
-  Houses Shell [gang No.]
-  Apartment SFS/Windows
-  Mast Climbers Installed [43-47]
-  Internal fitout commences week 40
-  Internal Fitout commences week 43
-  Hoist installed

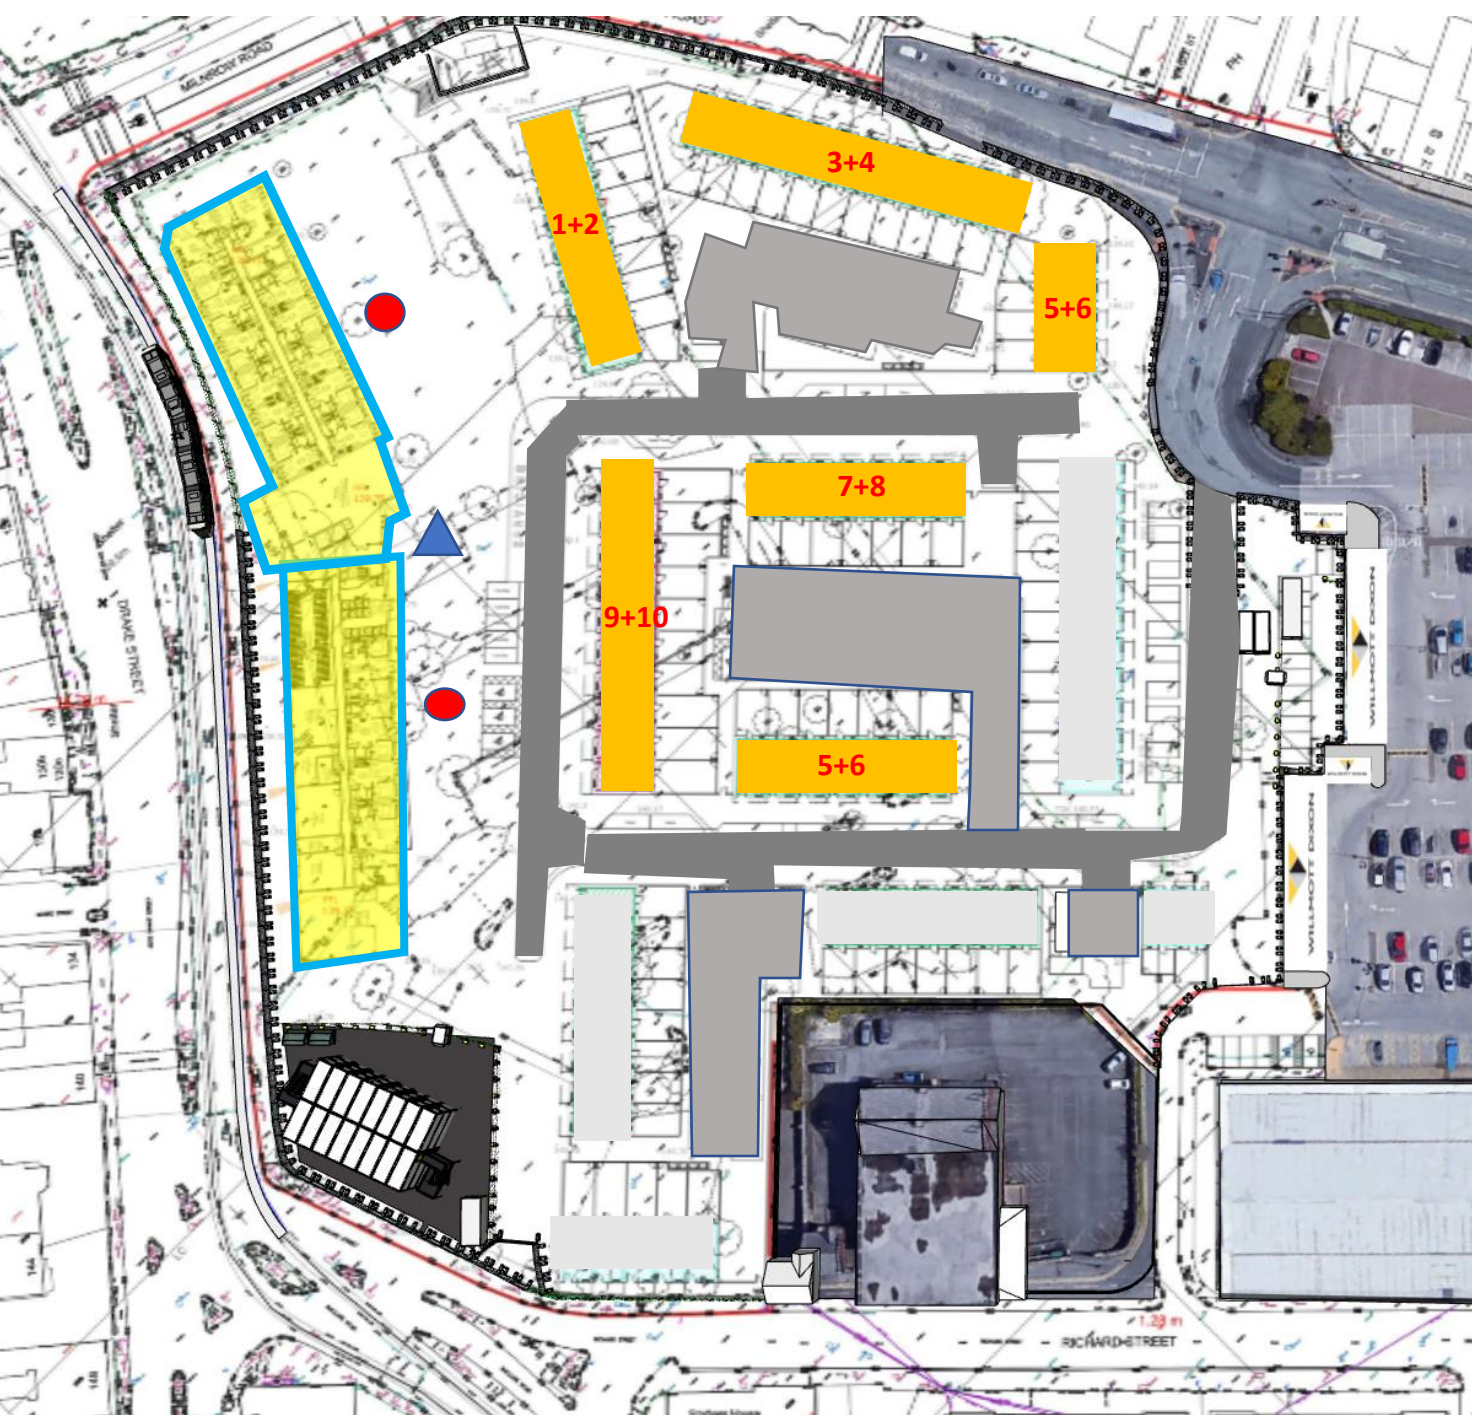

Week 47-52

-  House Substructure complete week 52
-  RC Frame Completed
South wing week 48
North wing Week 50
-  Houses Shell [gang No.]
-  Apartment SFS/Windows

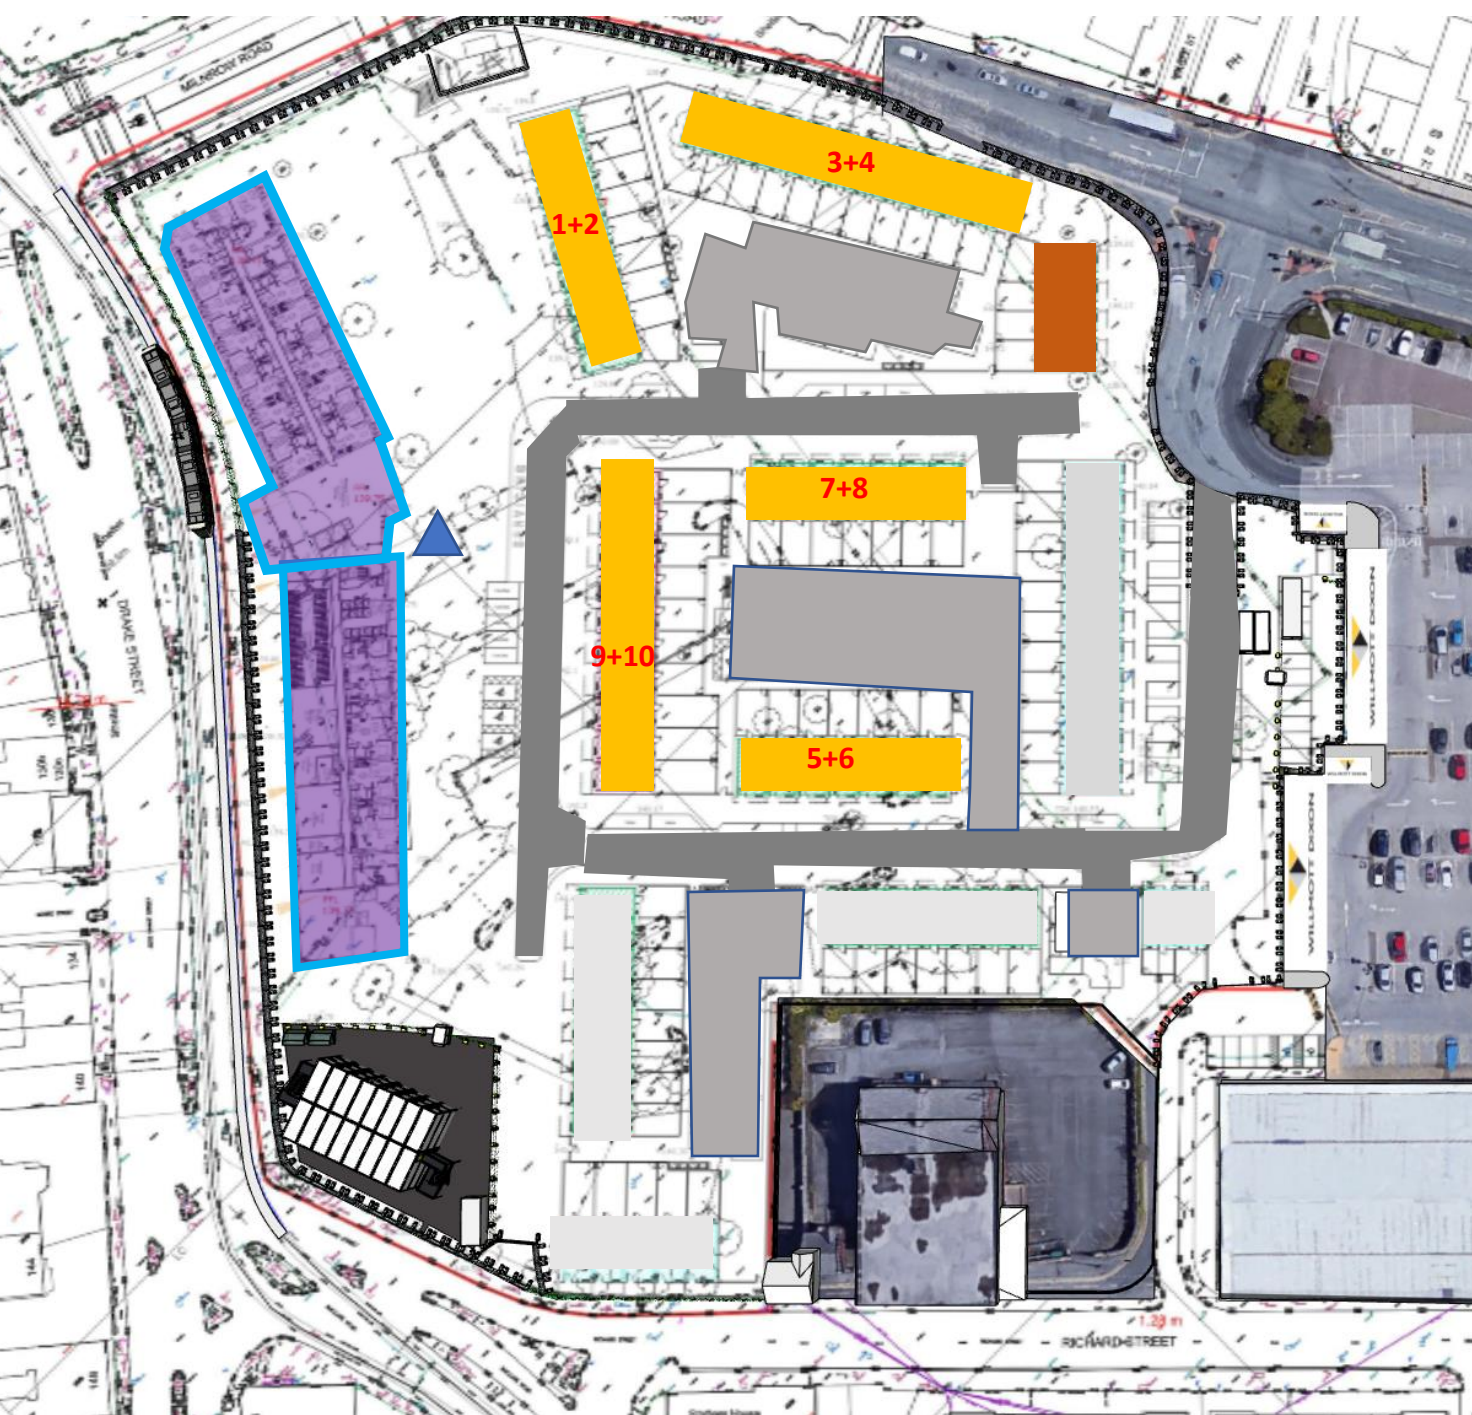

Week 52-57



Station Gardens
Rochdale

 Houses Shell [gang No.]


 Apartment SFS/Windows complete

 Apartment Brickwork

 Flat Roof Covering

 Tower crane removed

 Roof Timbers

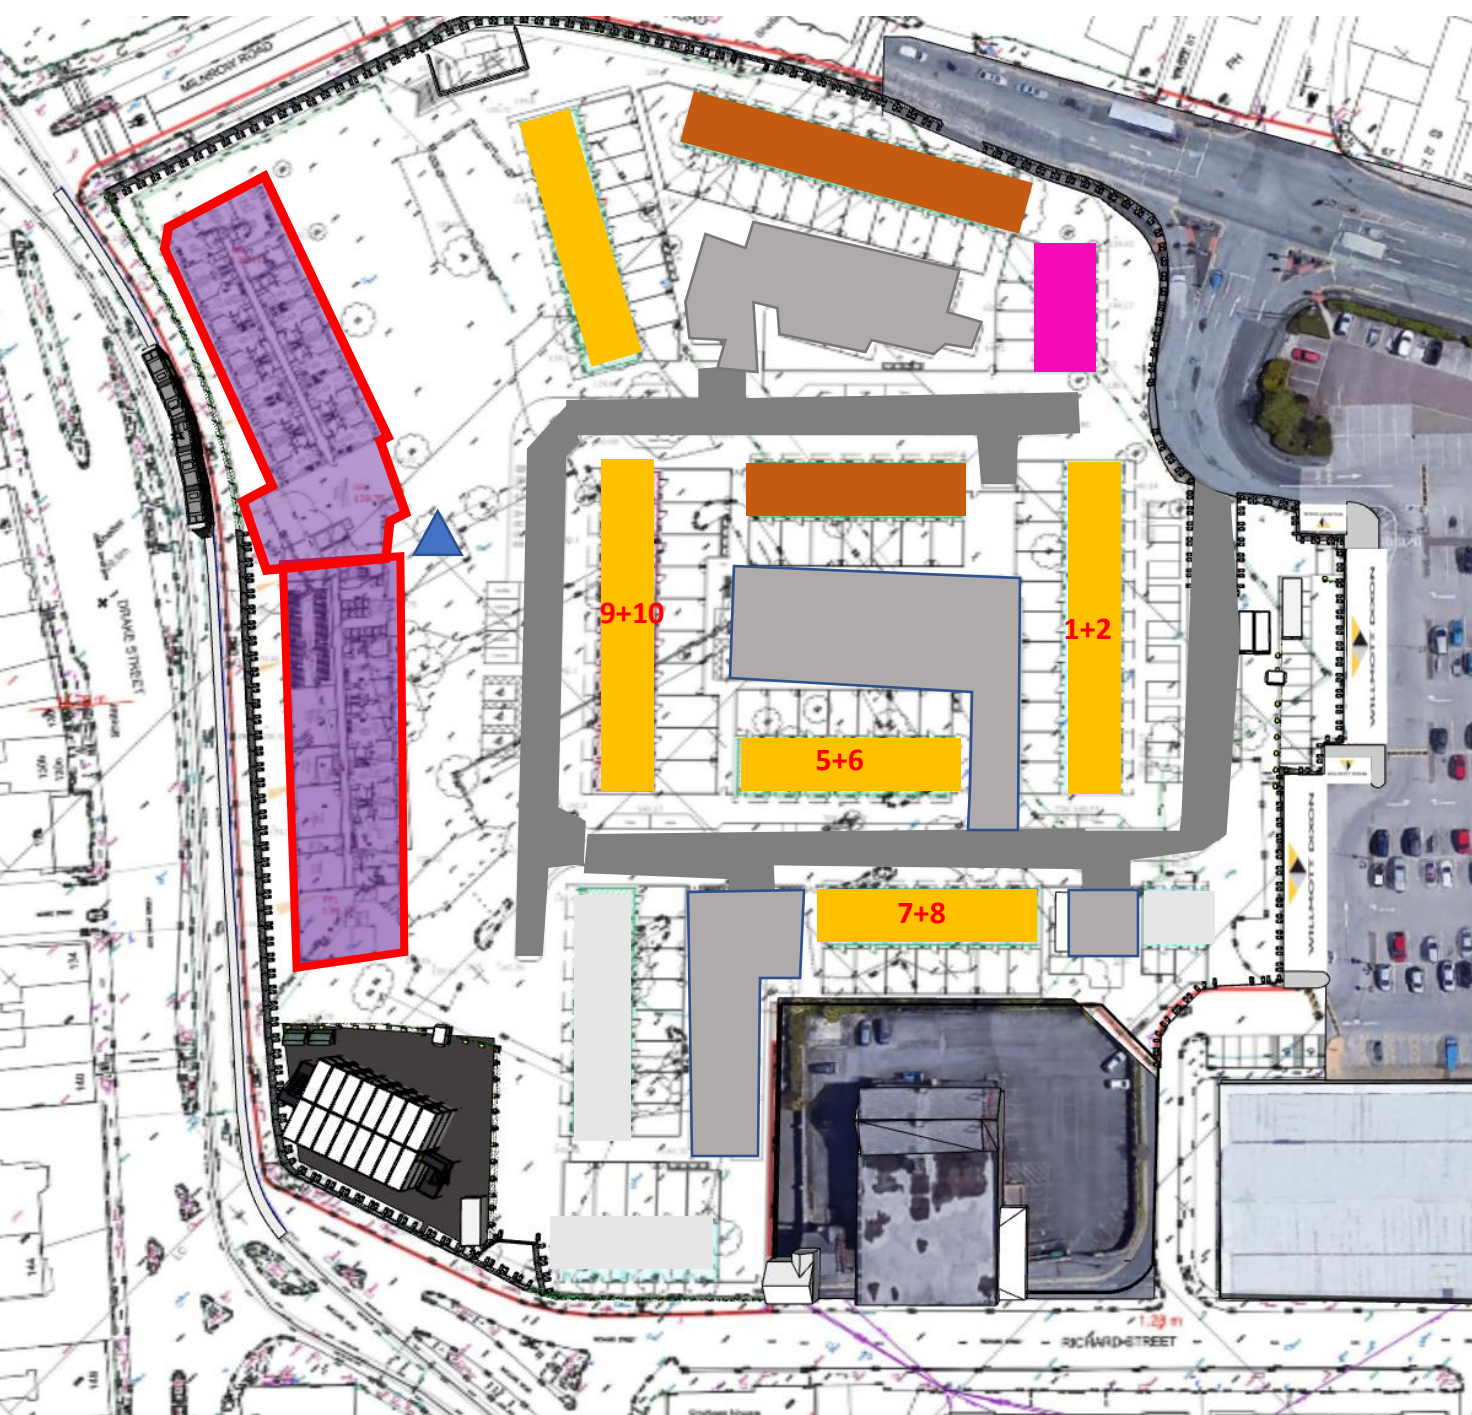

Week 57-61



Station Gardens
Rochdale


 Houses Shell [gang No.]

 Apartment Brickwork

 Flat Roof Covering complete
North wing week 57
South wing week 61


 Roof Timbers

 Tiled Roofing

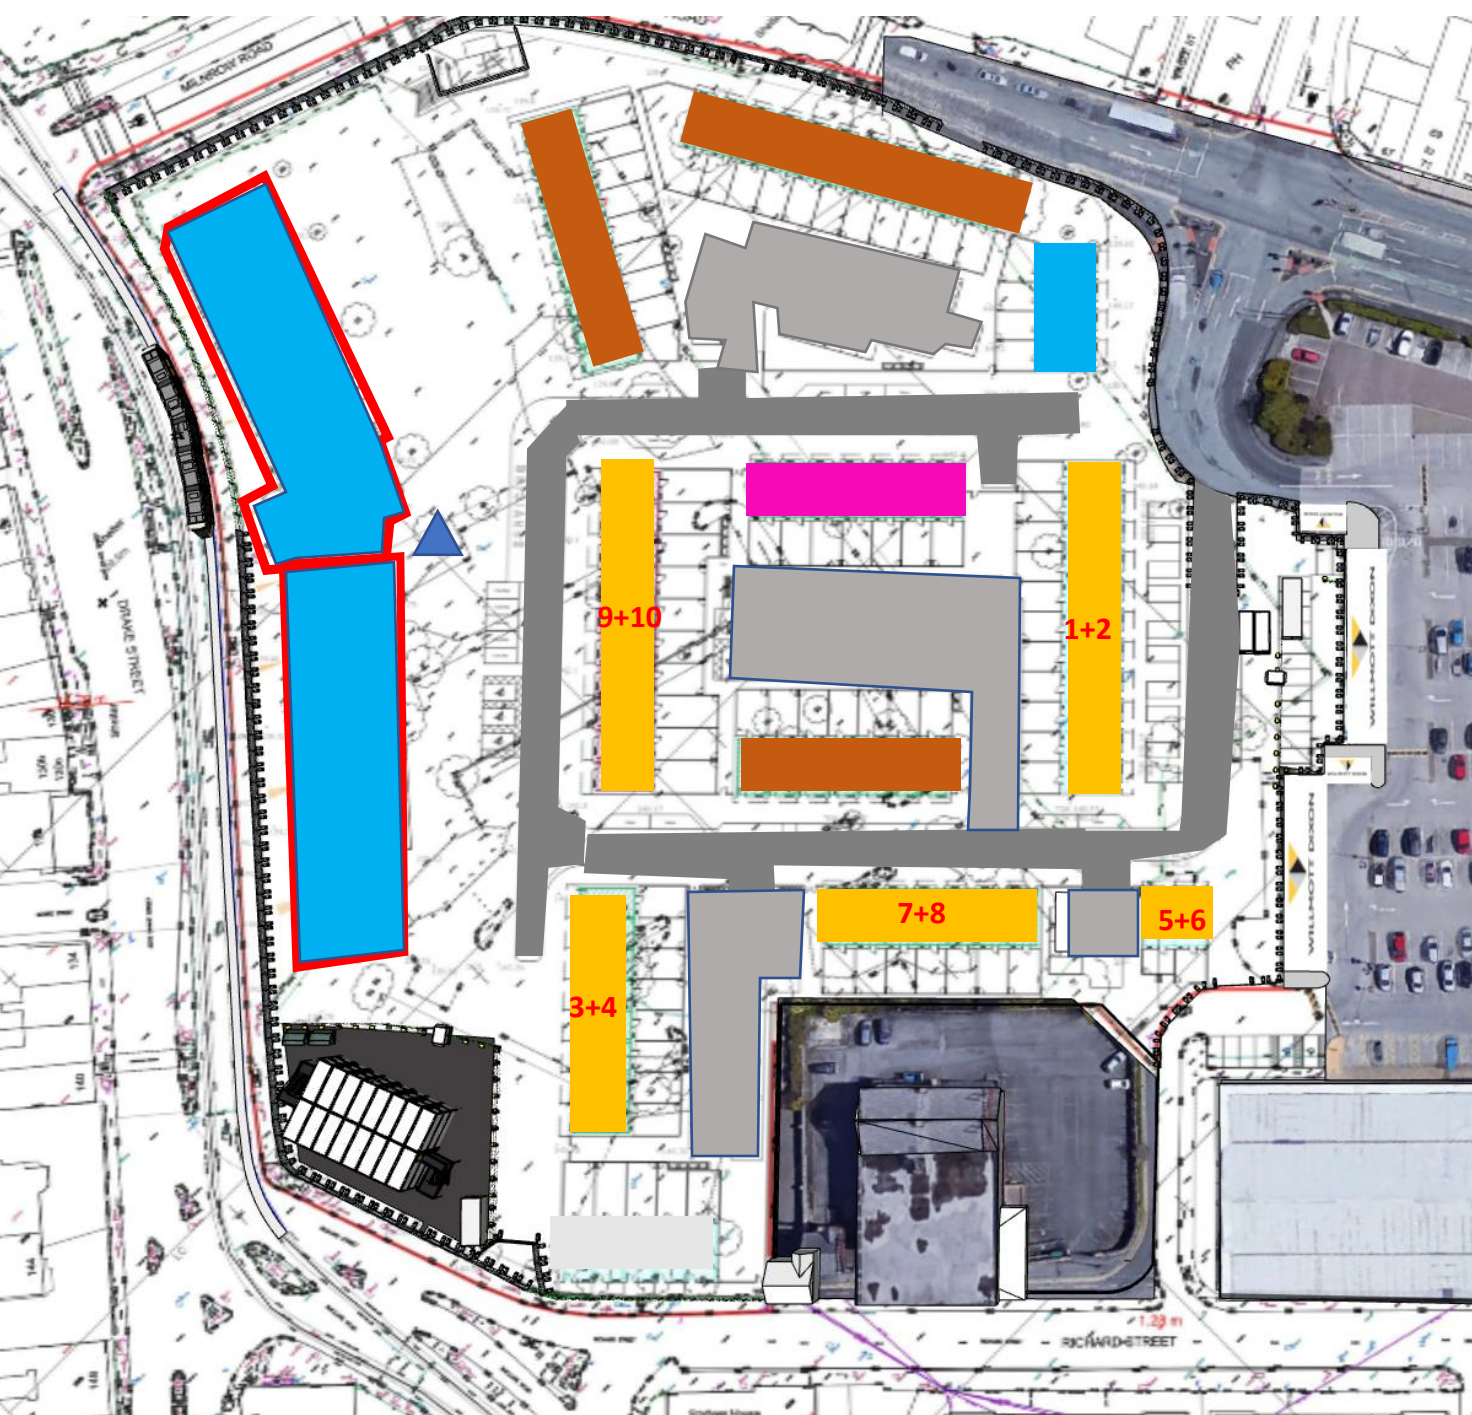

Week 55-60

-  Houses Shell [gang No.]
-  Apartment Brickwork
-  Roof Timbers
-  Tiled Roofing
-  Finishes

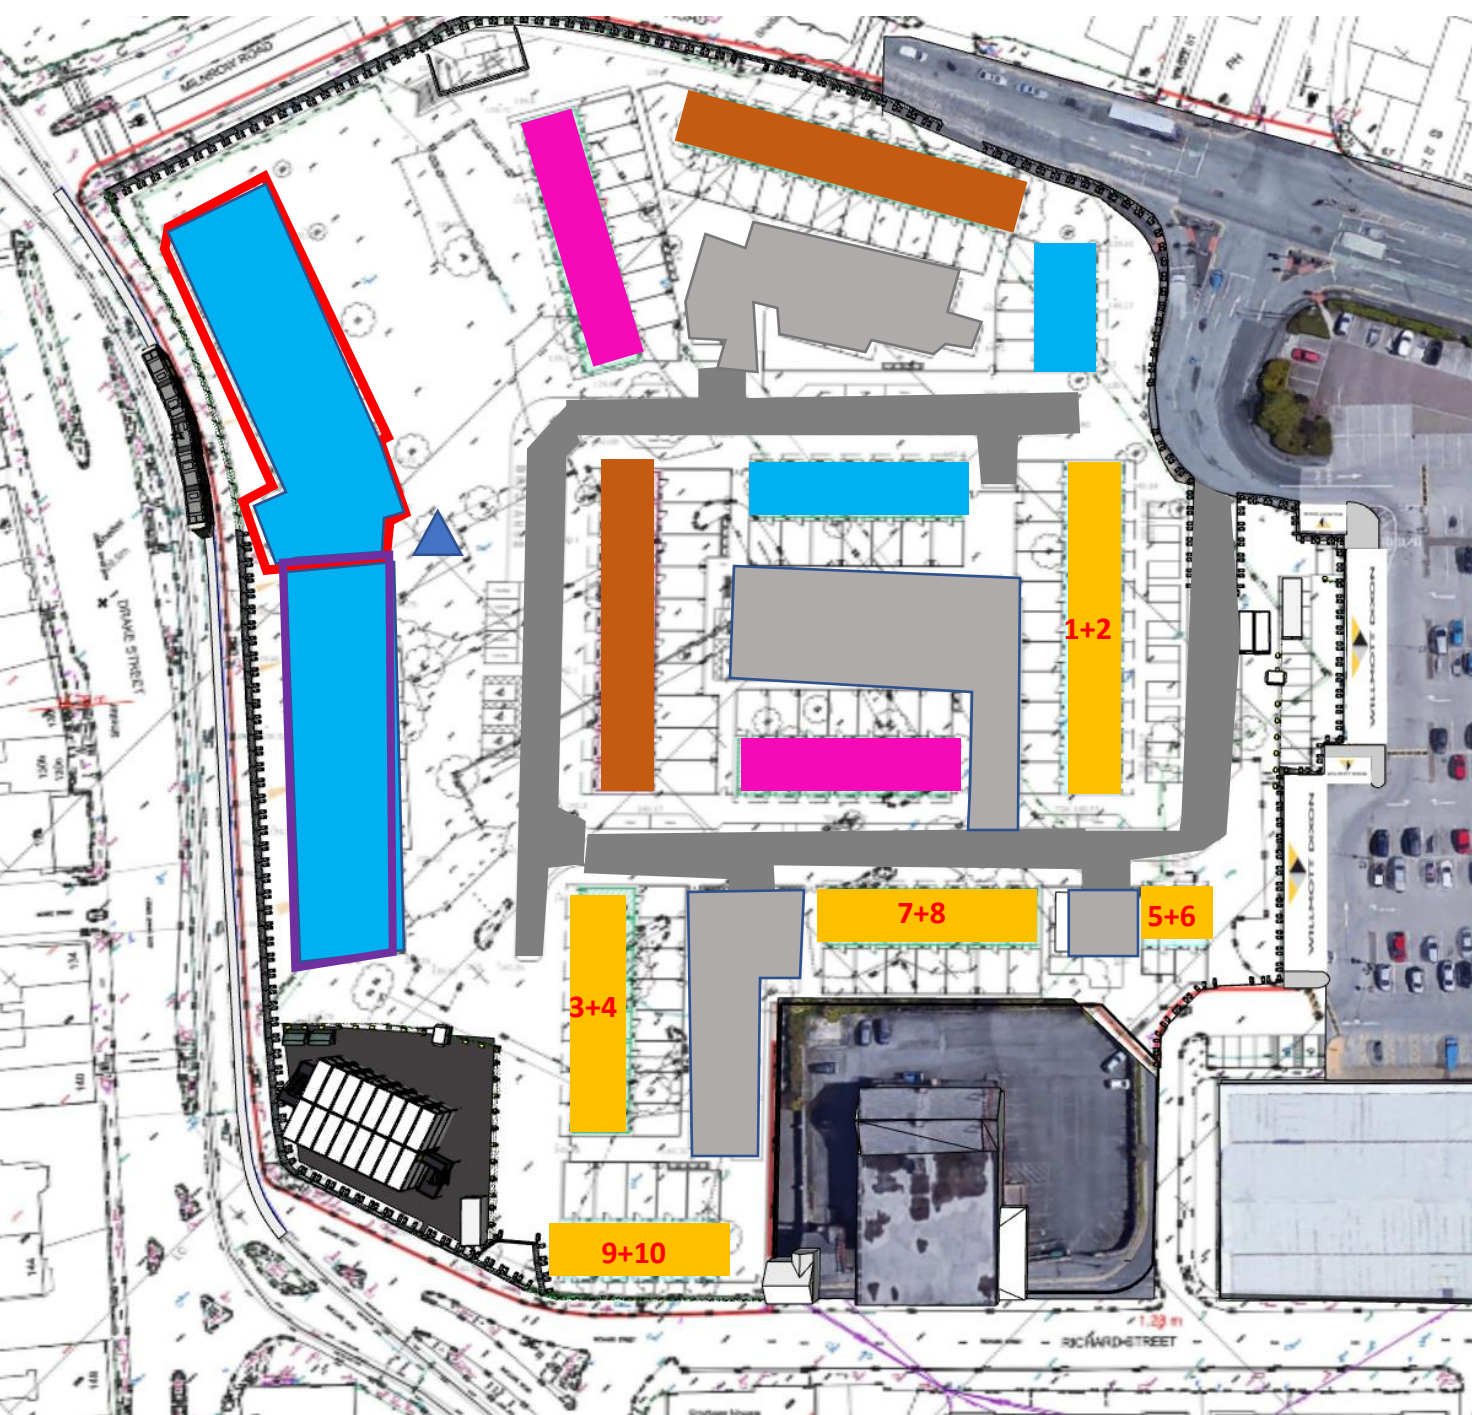

Week 60-65



Houses Shell [gang No.]



Apartment Brickwork



Complete envelope to first floor and
install balconies



Roof Timbers




Tiled Roofing



Finishes



Station Gardens
Rochdale

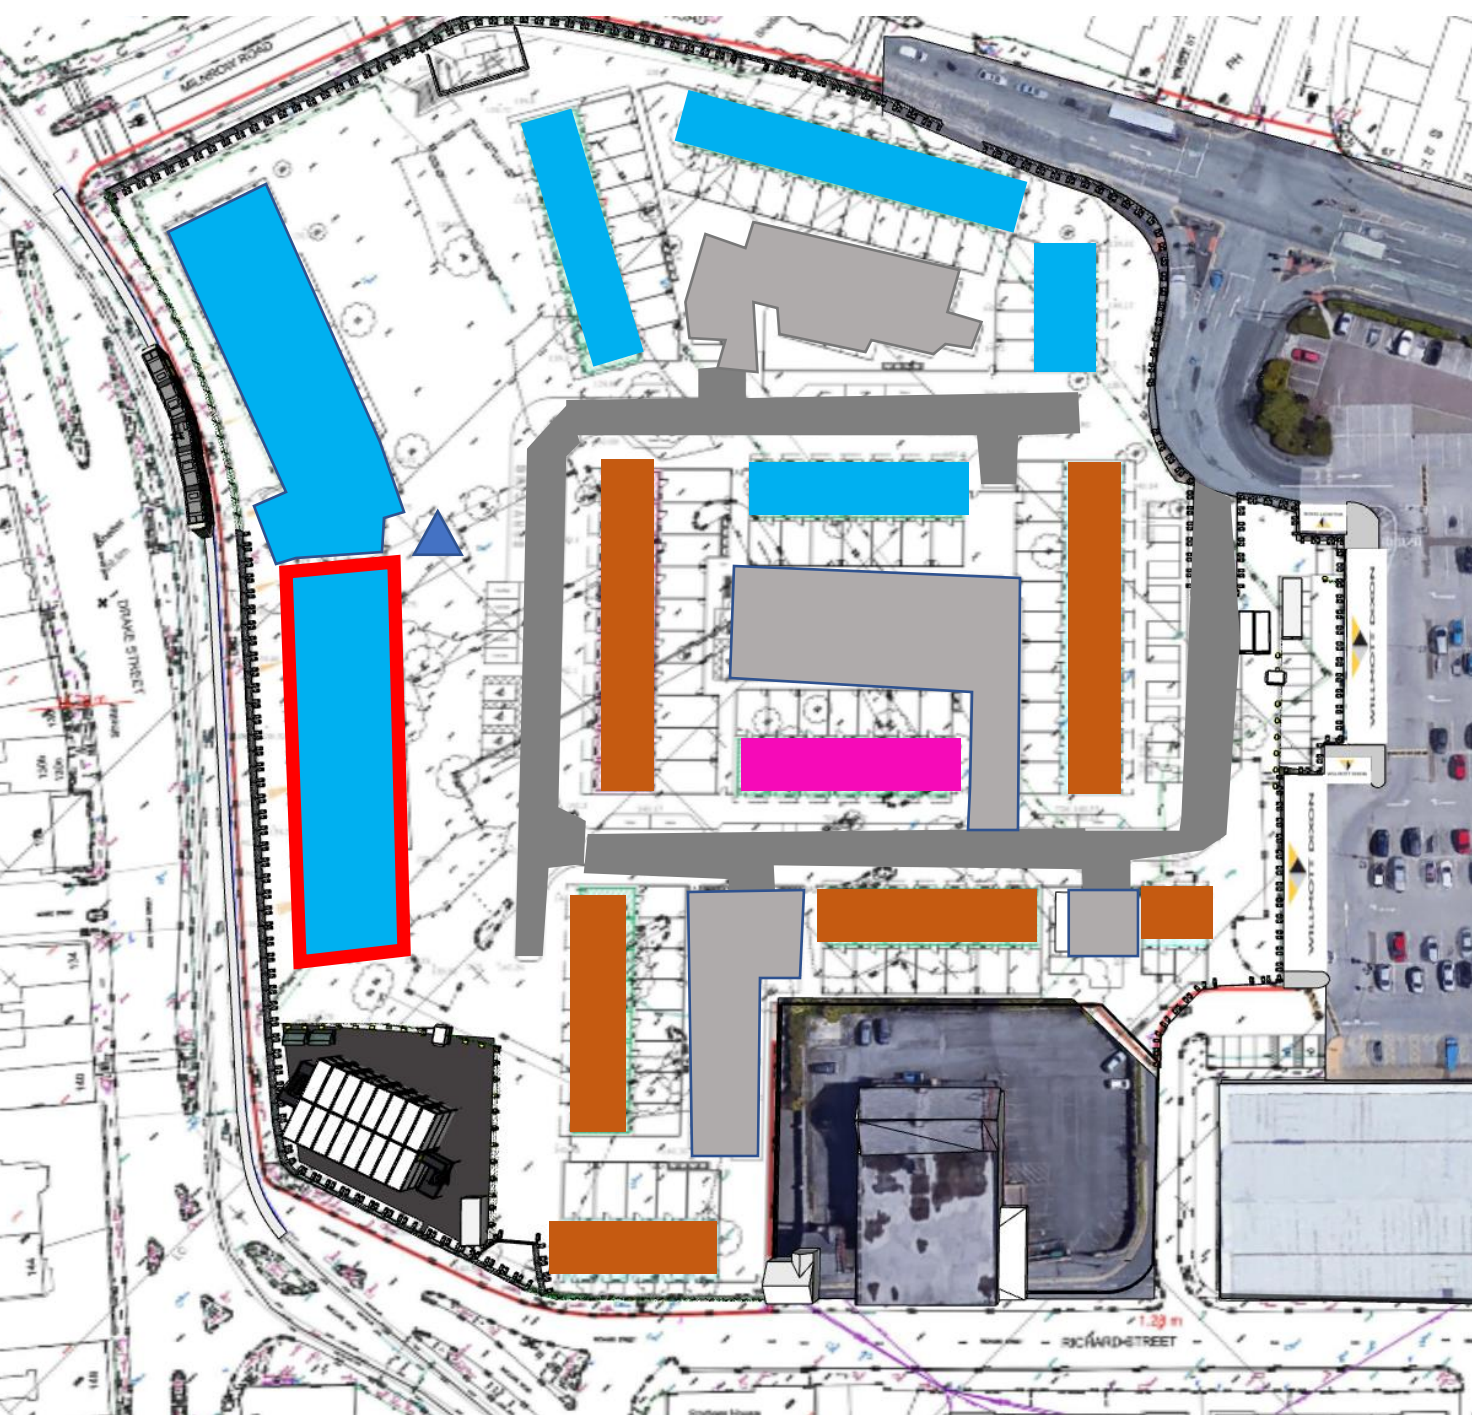

Week 65-75



**Apartment Brickwork
South Wing Complete Week 75**



Roof Timbers



Tiled Roofing




Finishes



External Works



**Station Gardens
Rochdale**

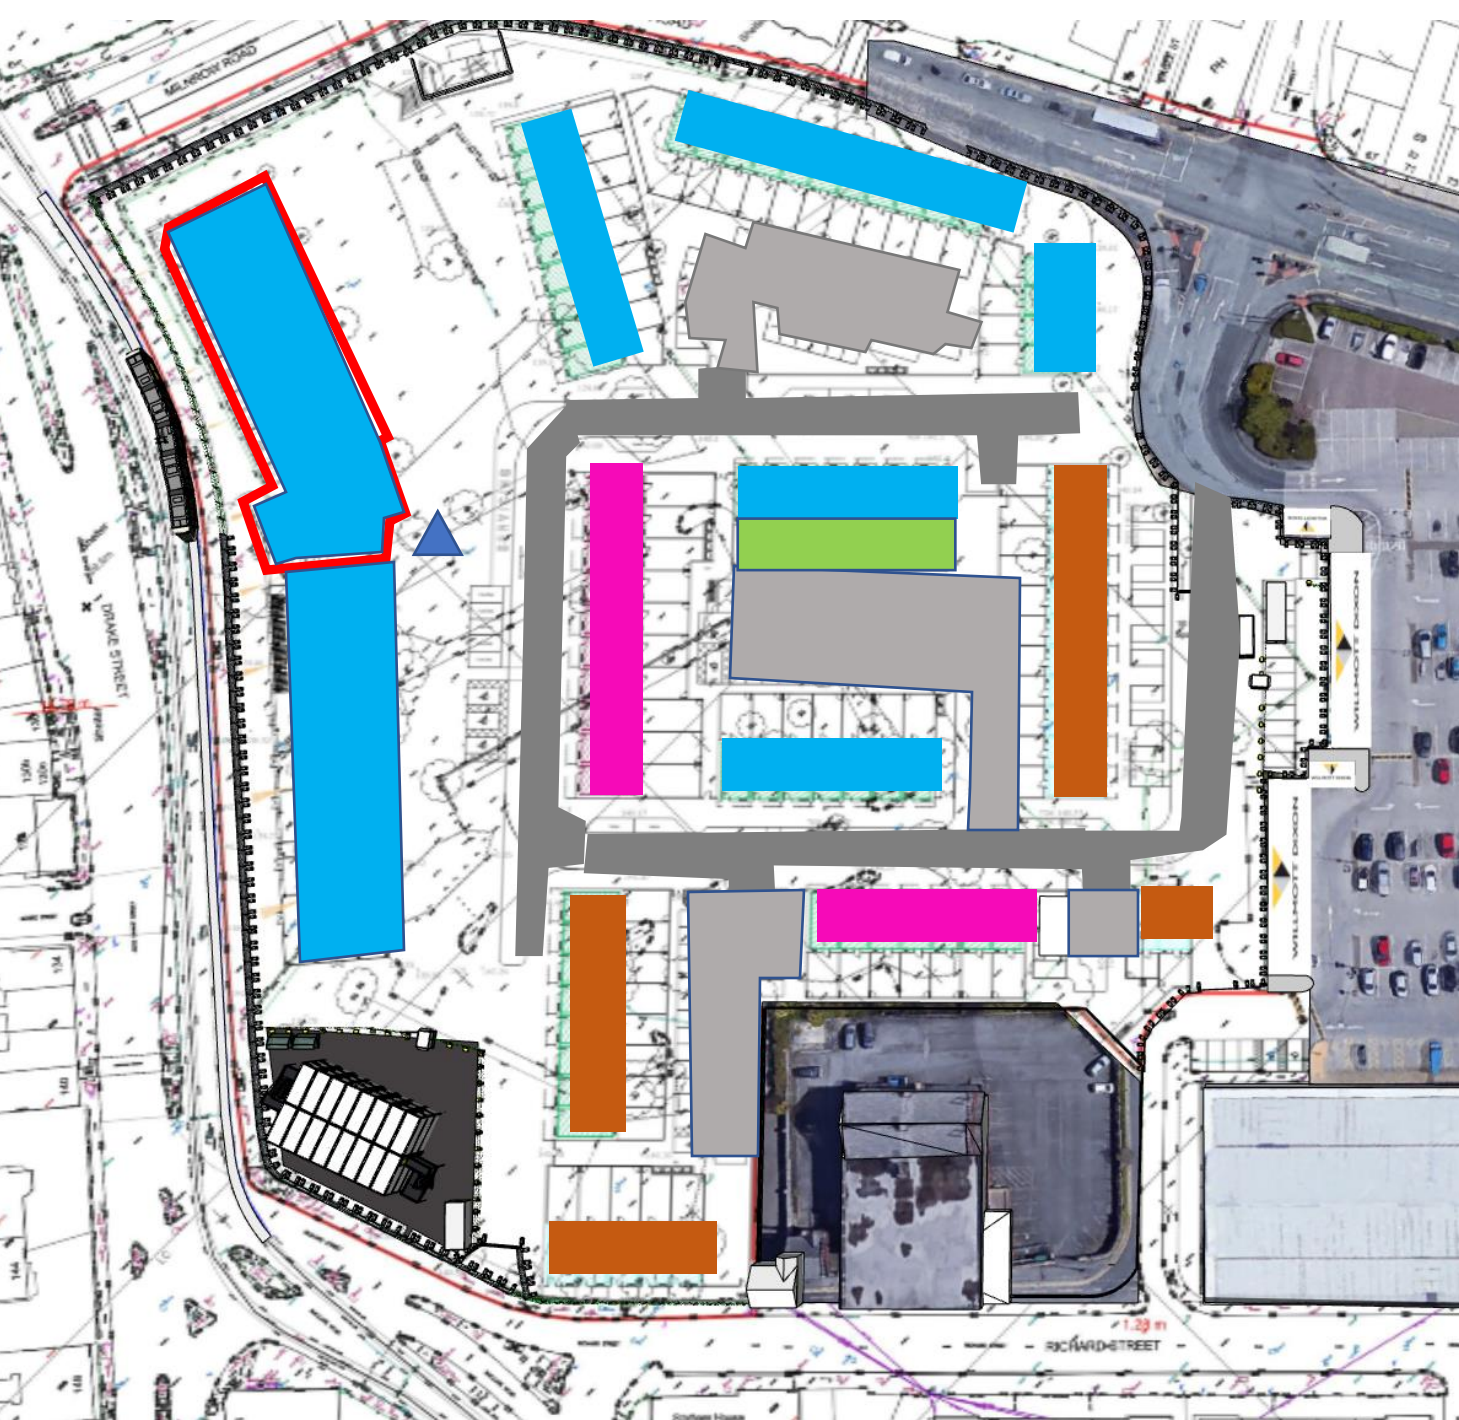

Week 75-81



Brickwork Complete
North Wing Week 81




Roof Timbers



Tiled Roofing




Finishes

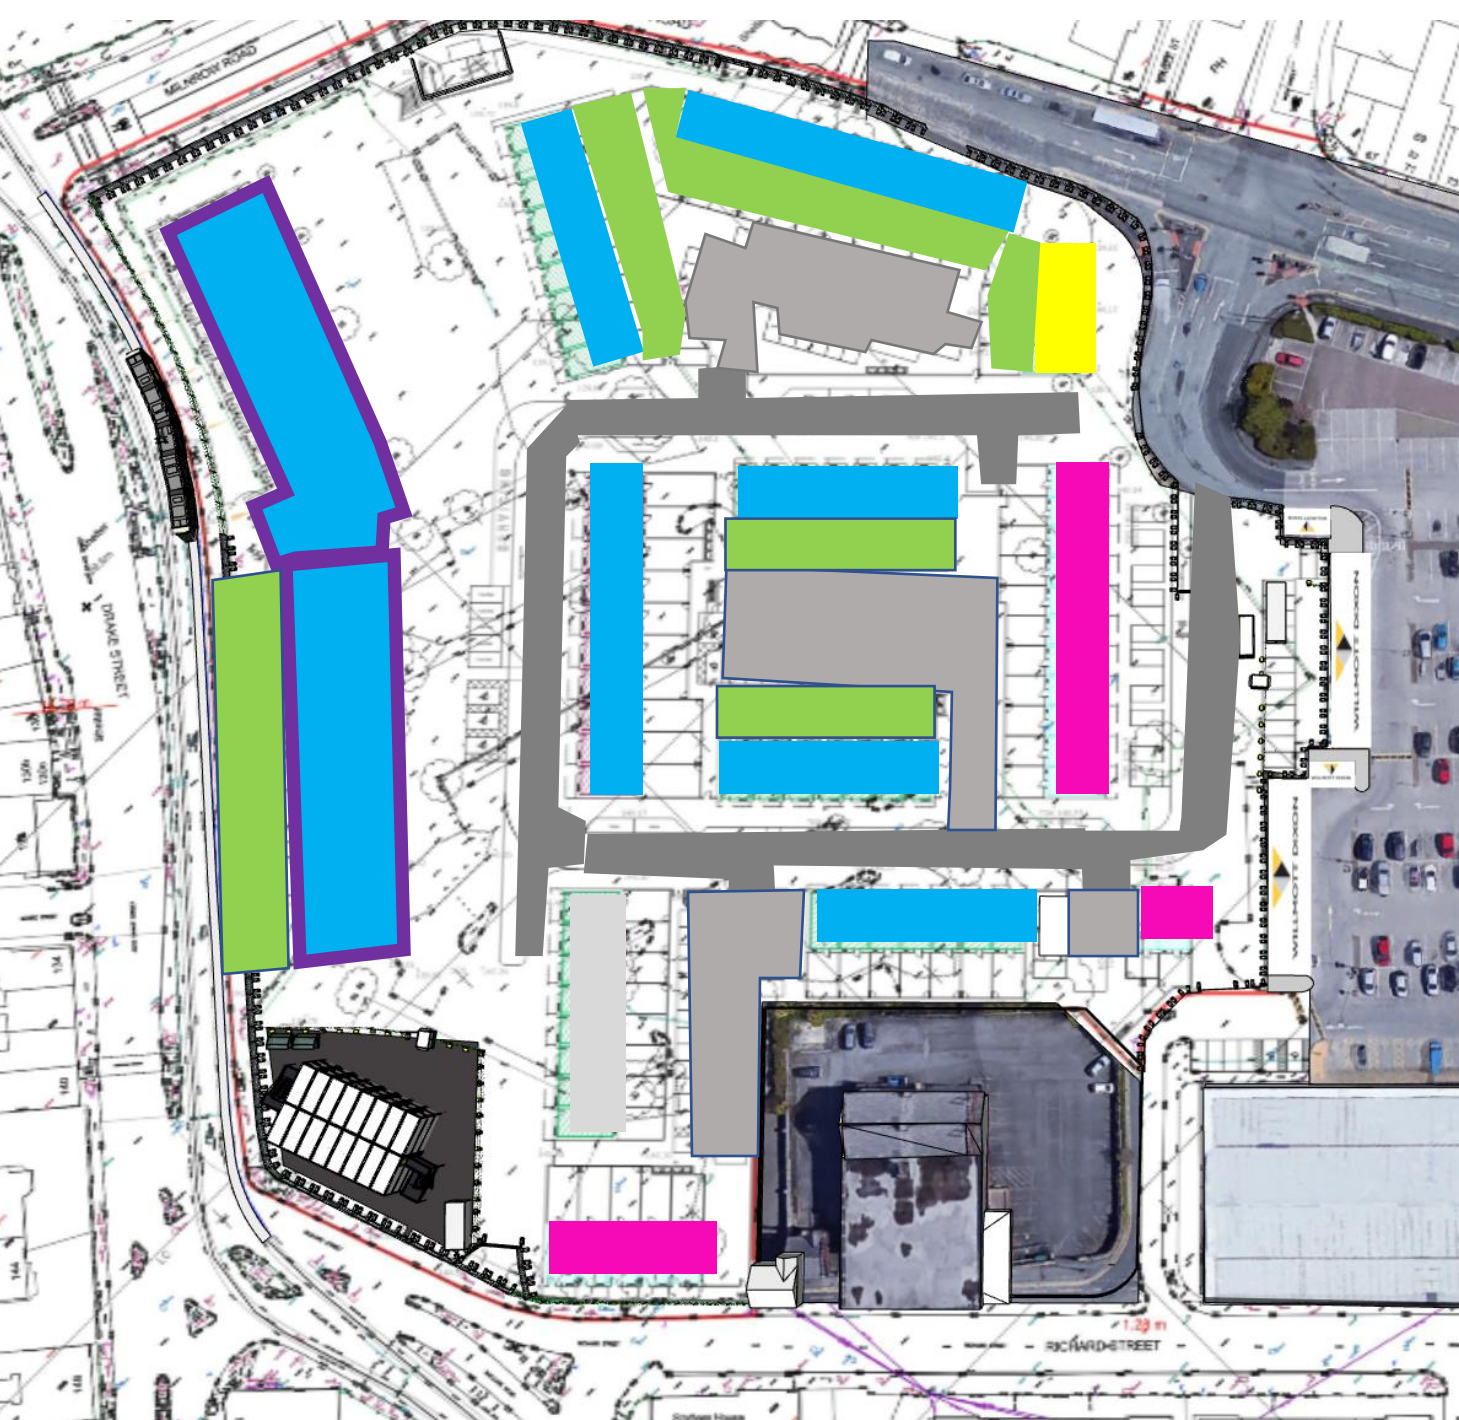

Week 77-81

-  Tiled Roofing
-  Finishes
-  External Works
-  Units complete
-  Hoist Removed week 77
-  Balconies Installed

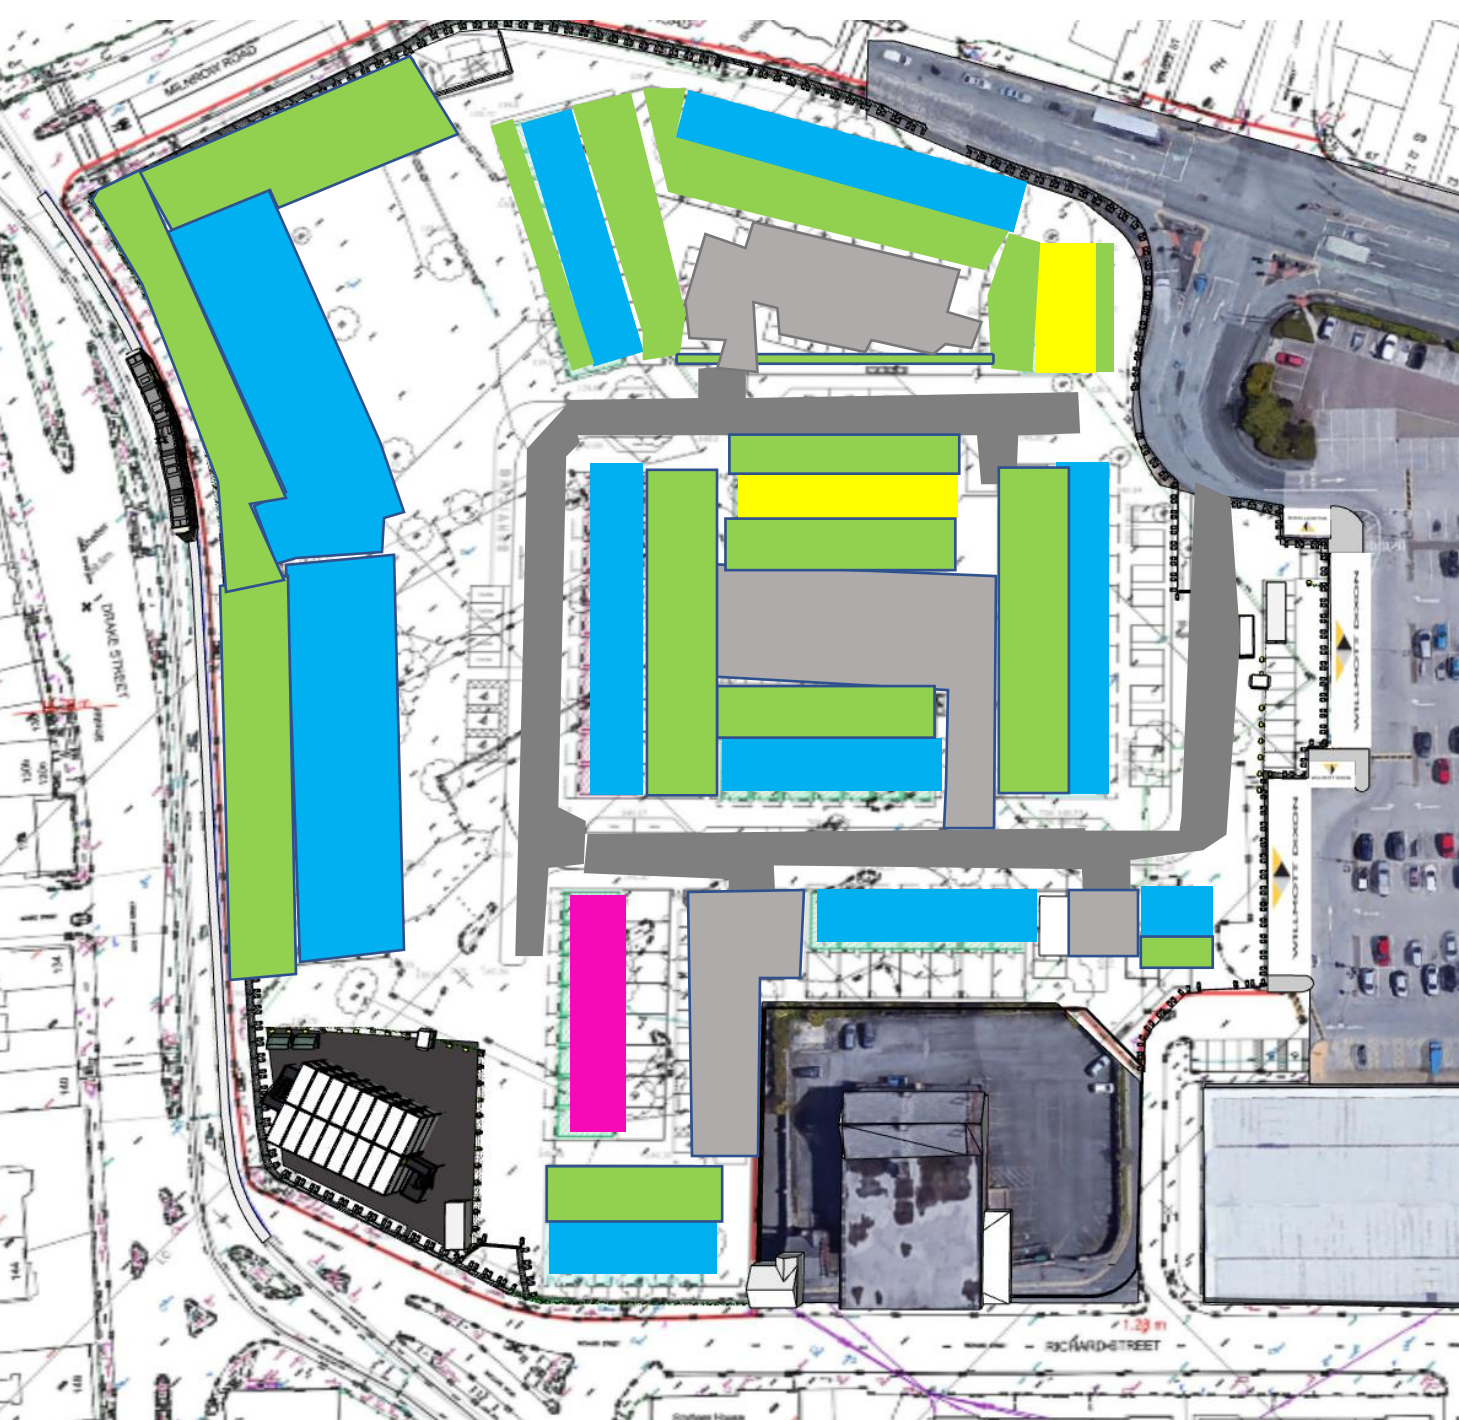

Week 81-87



Tiled Roof



Finishes




External Works




Units complete




**Station Gardens
Rochdale**

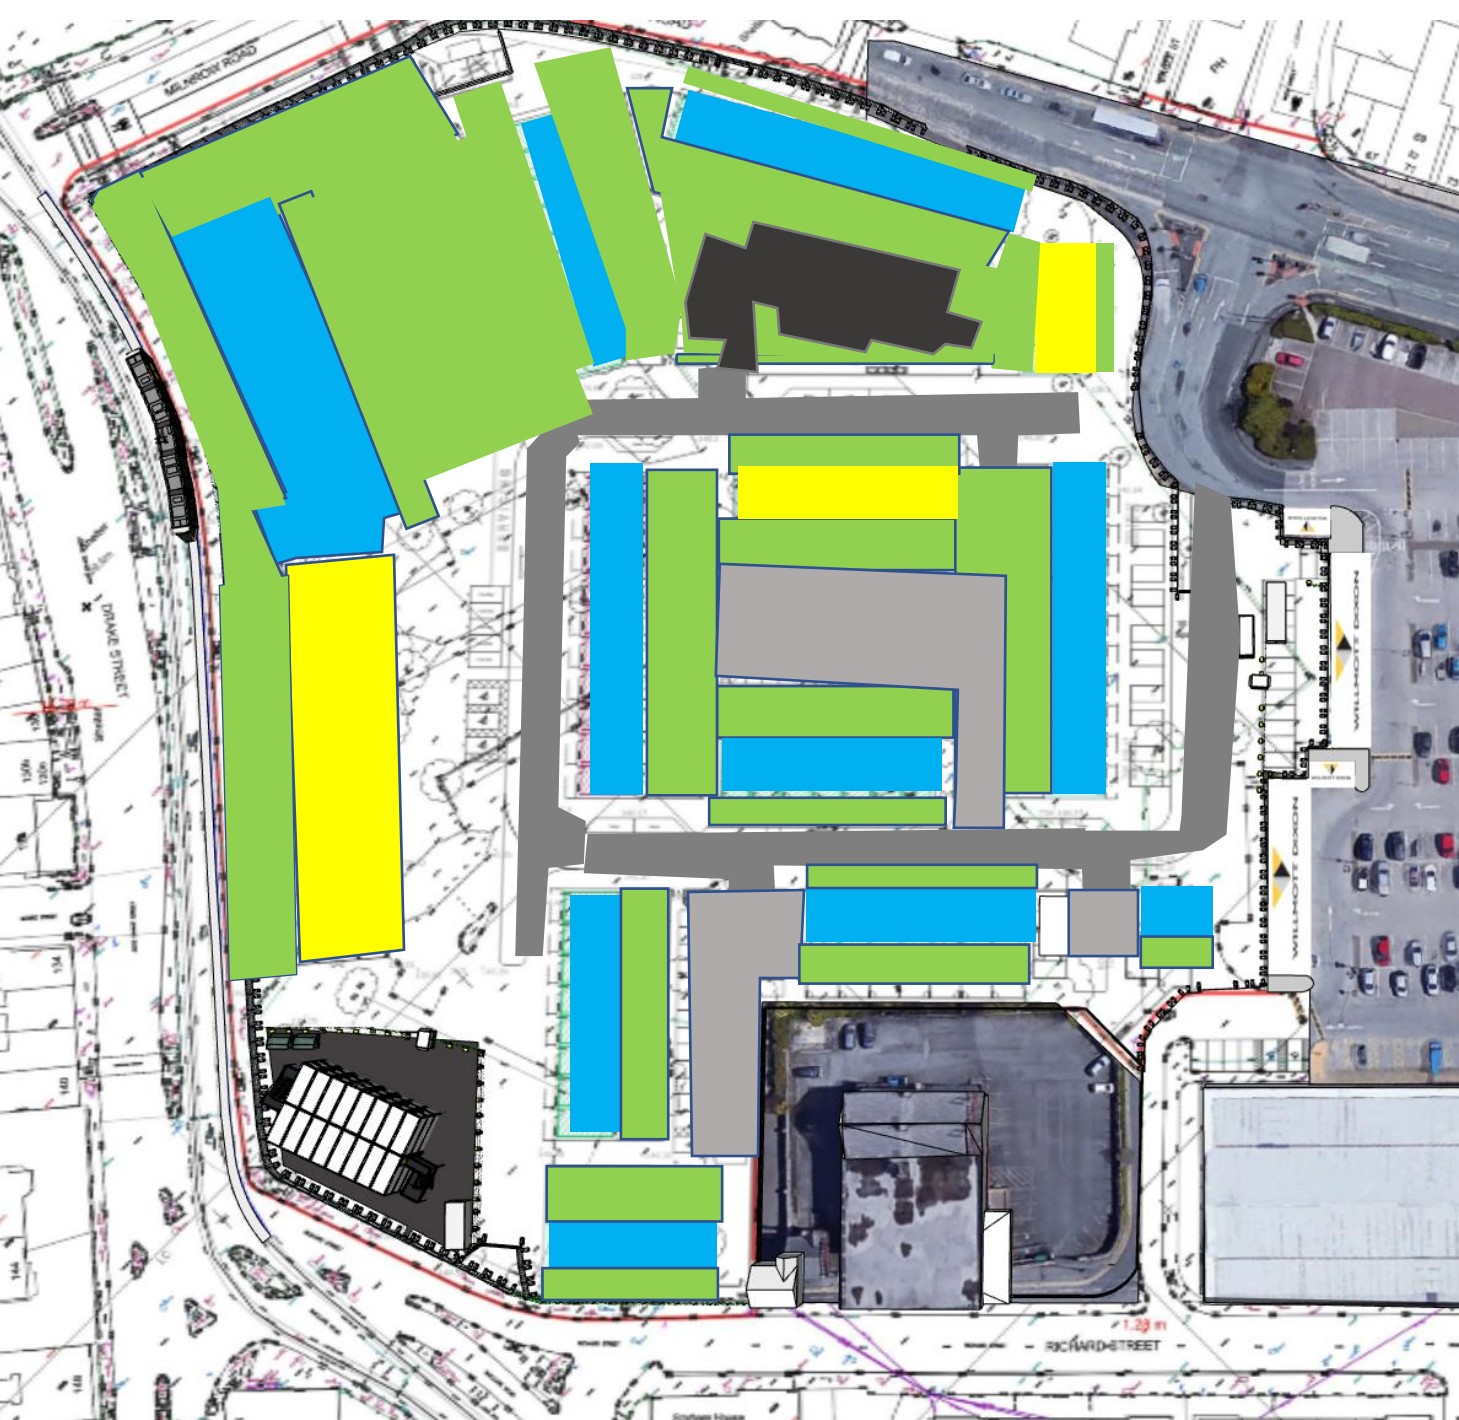

-  Finishes
-  External Works
-  Units complete
-  Tarmac/White line / clean

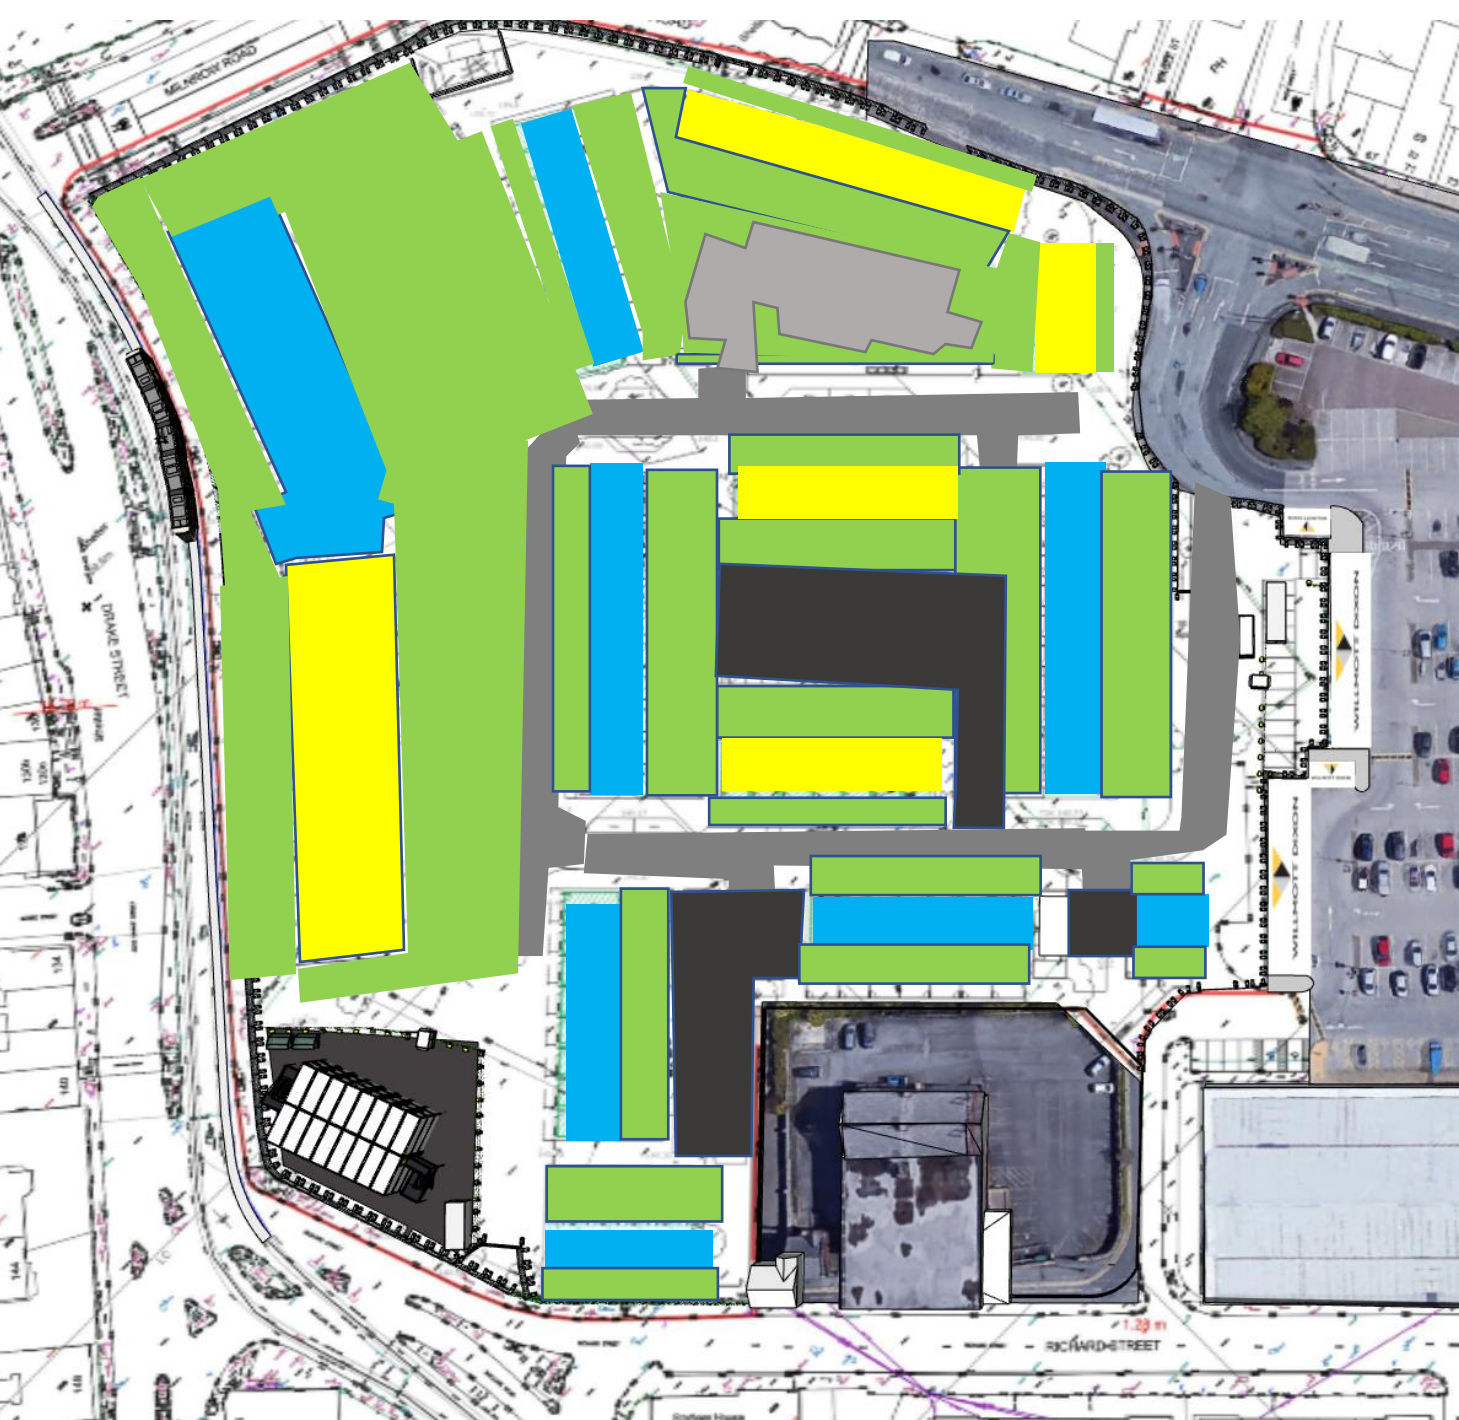

-  Finishes
-  External Works
-  Units complete
-  Tarmac/White line / clean

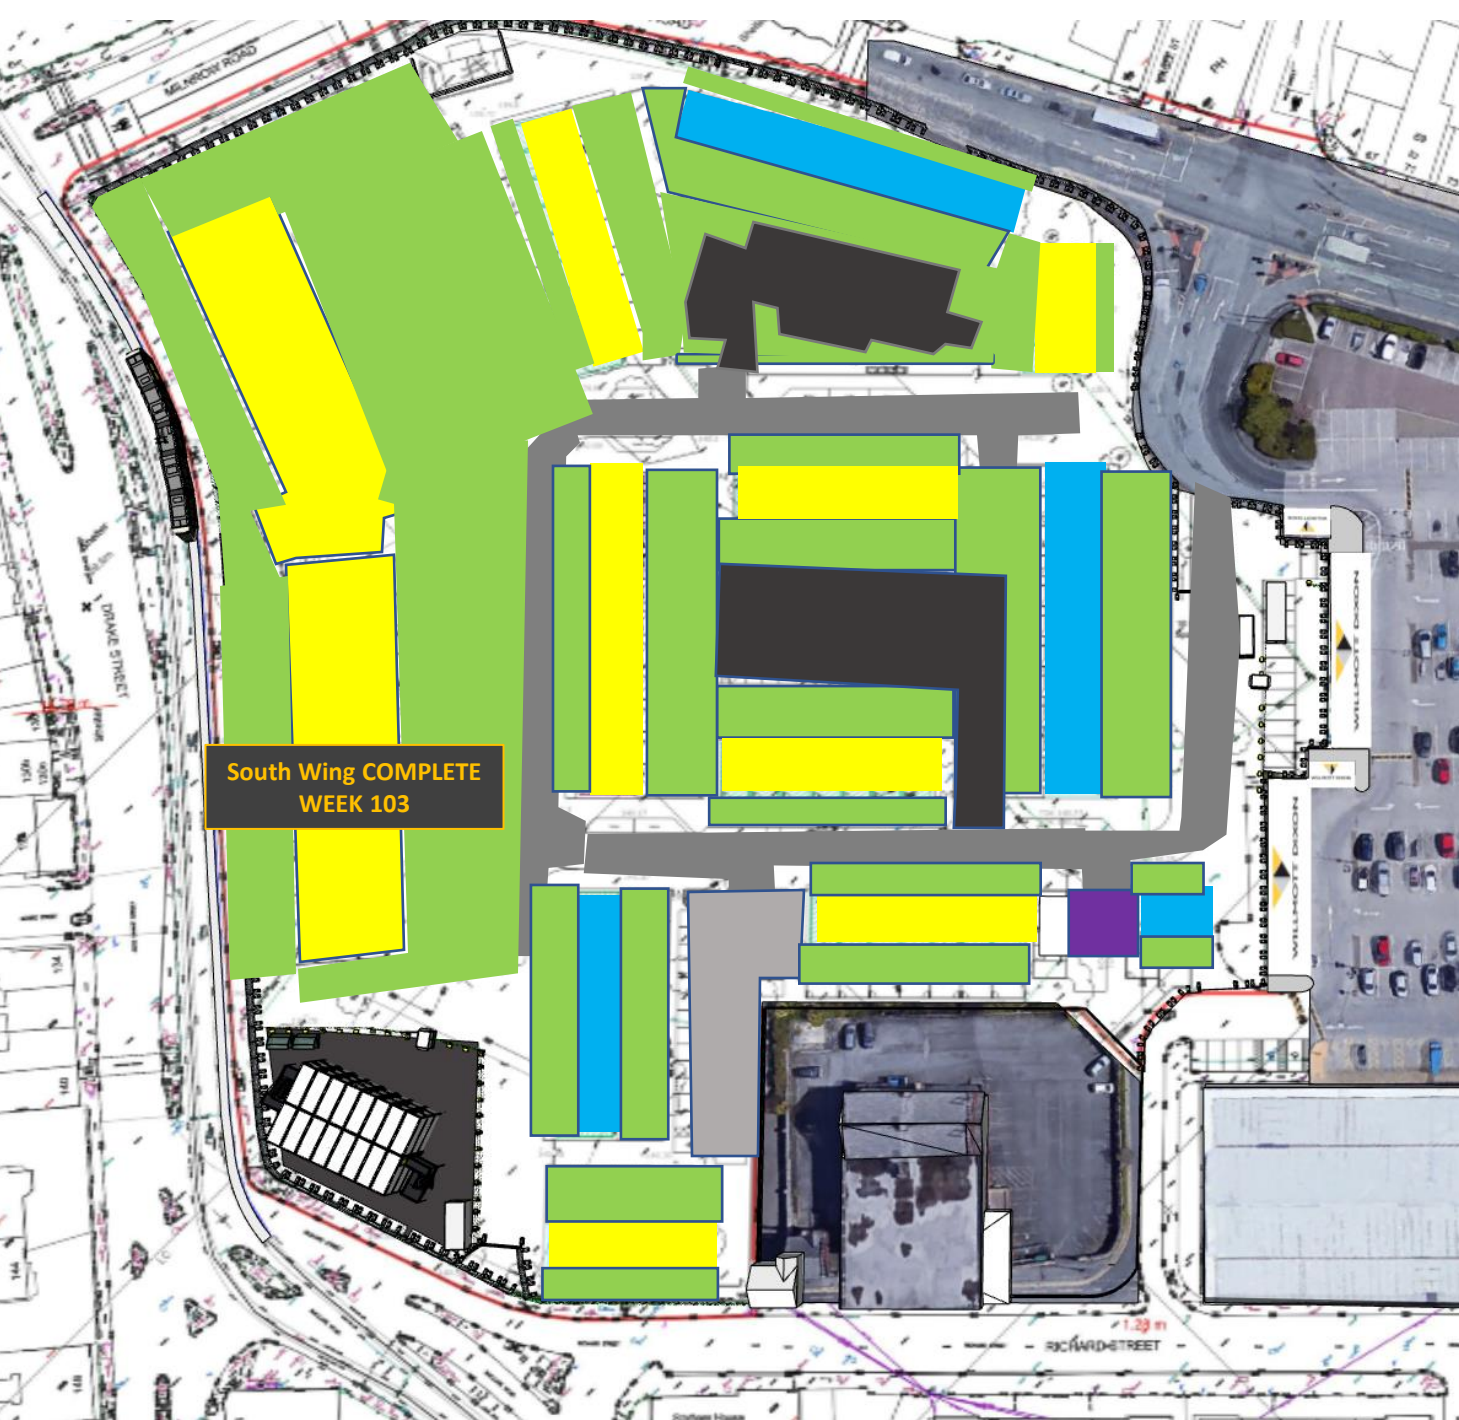

Week 95-103



Rochdale
Neighbourhood



Finishes



External Works




Units complete



Tarmac/White line / clean




Welfare Decanted

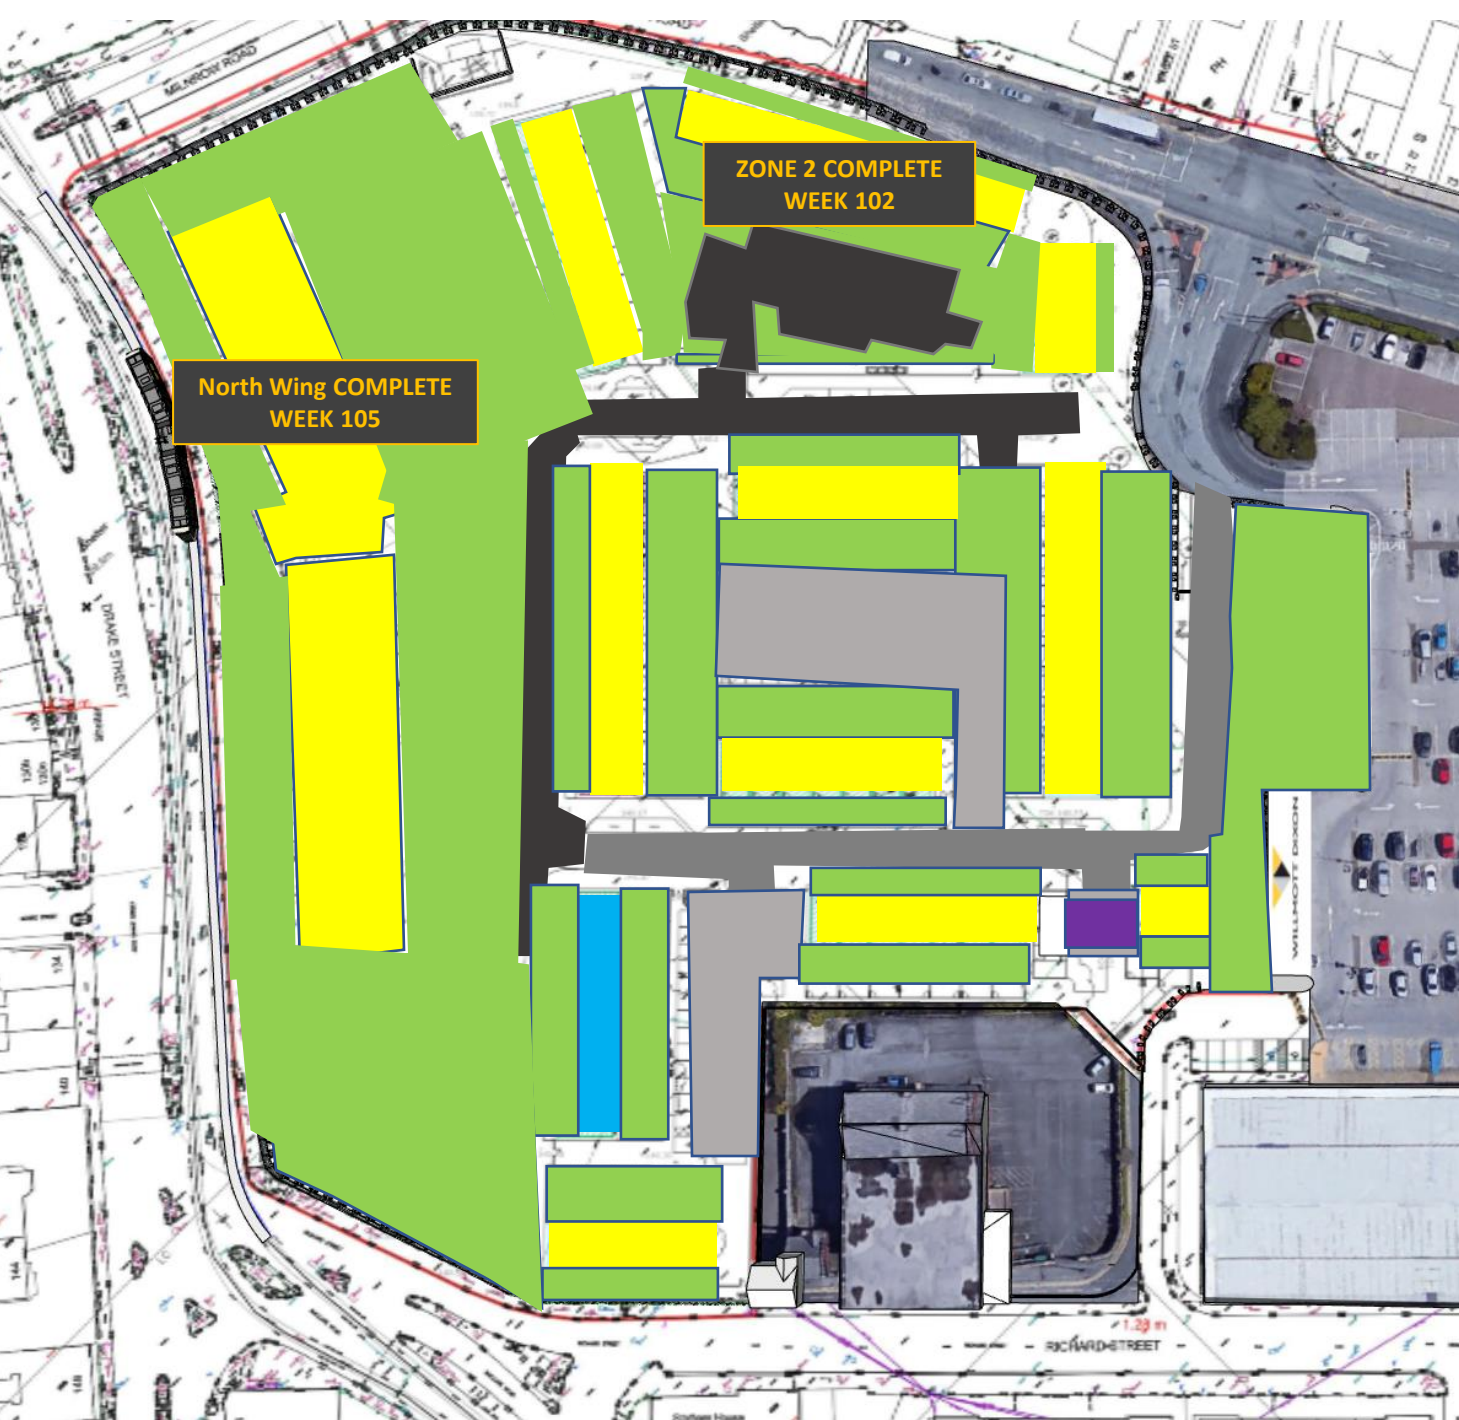

Week 103-105


-  Finishes
-  External Works
-  Units complete
-  Tarmac/White line / clean

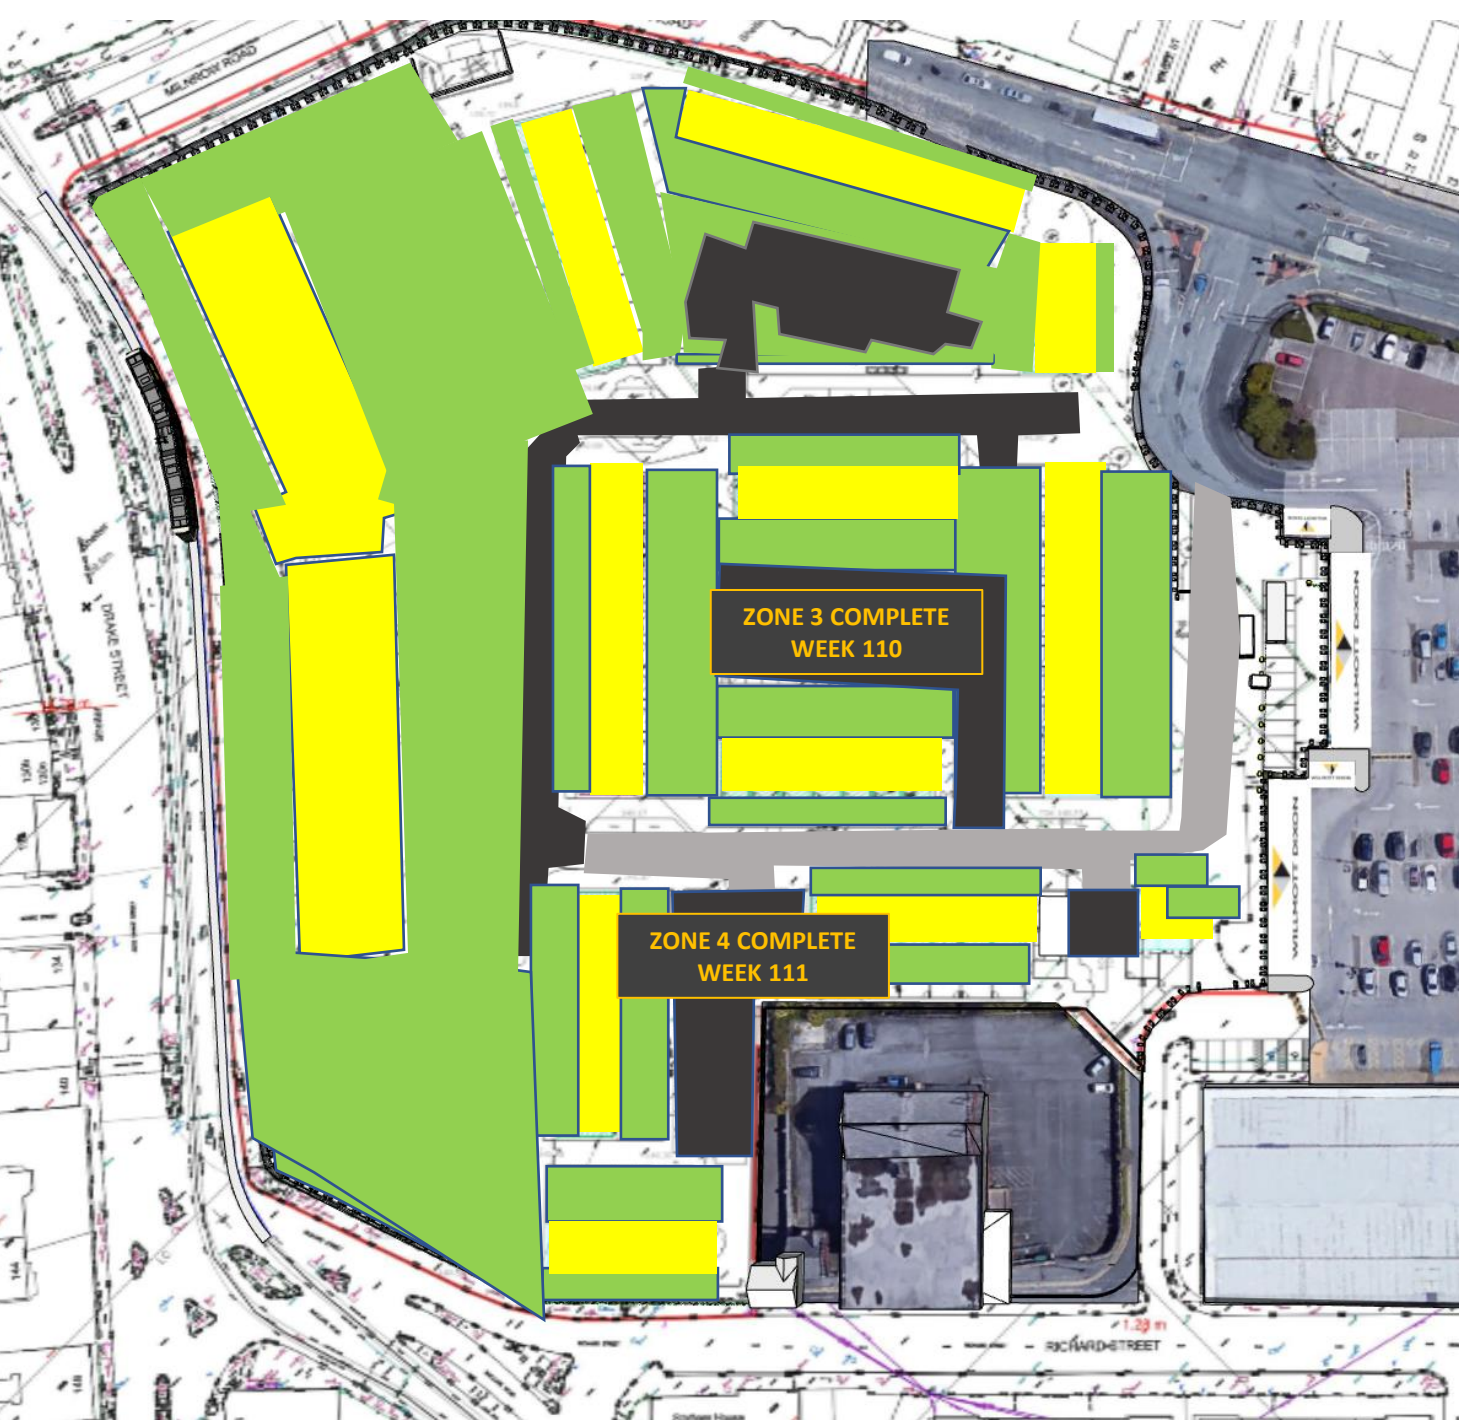


Week 105-111



Rochdale
Neighbourhood

-  Finishes
-  External Works
-  Units complete
-  Tarmac/White line / clean

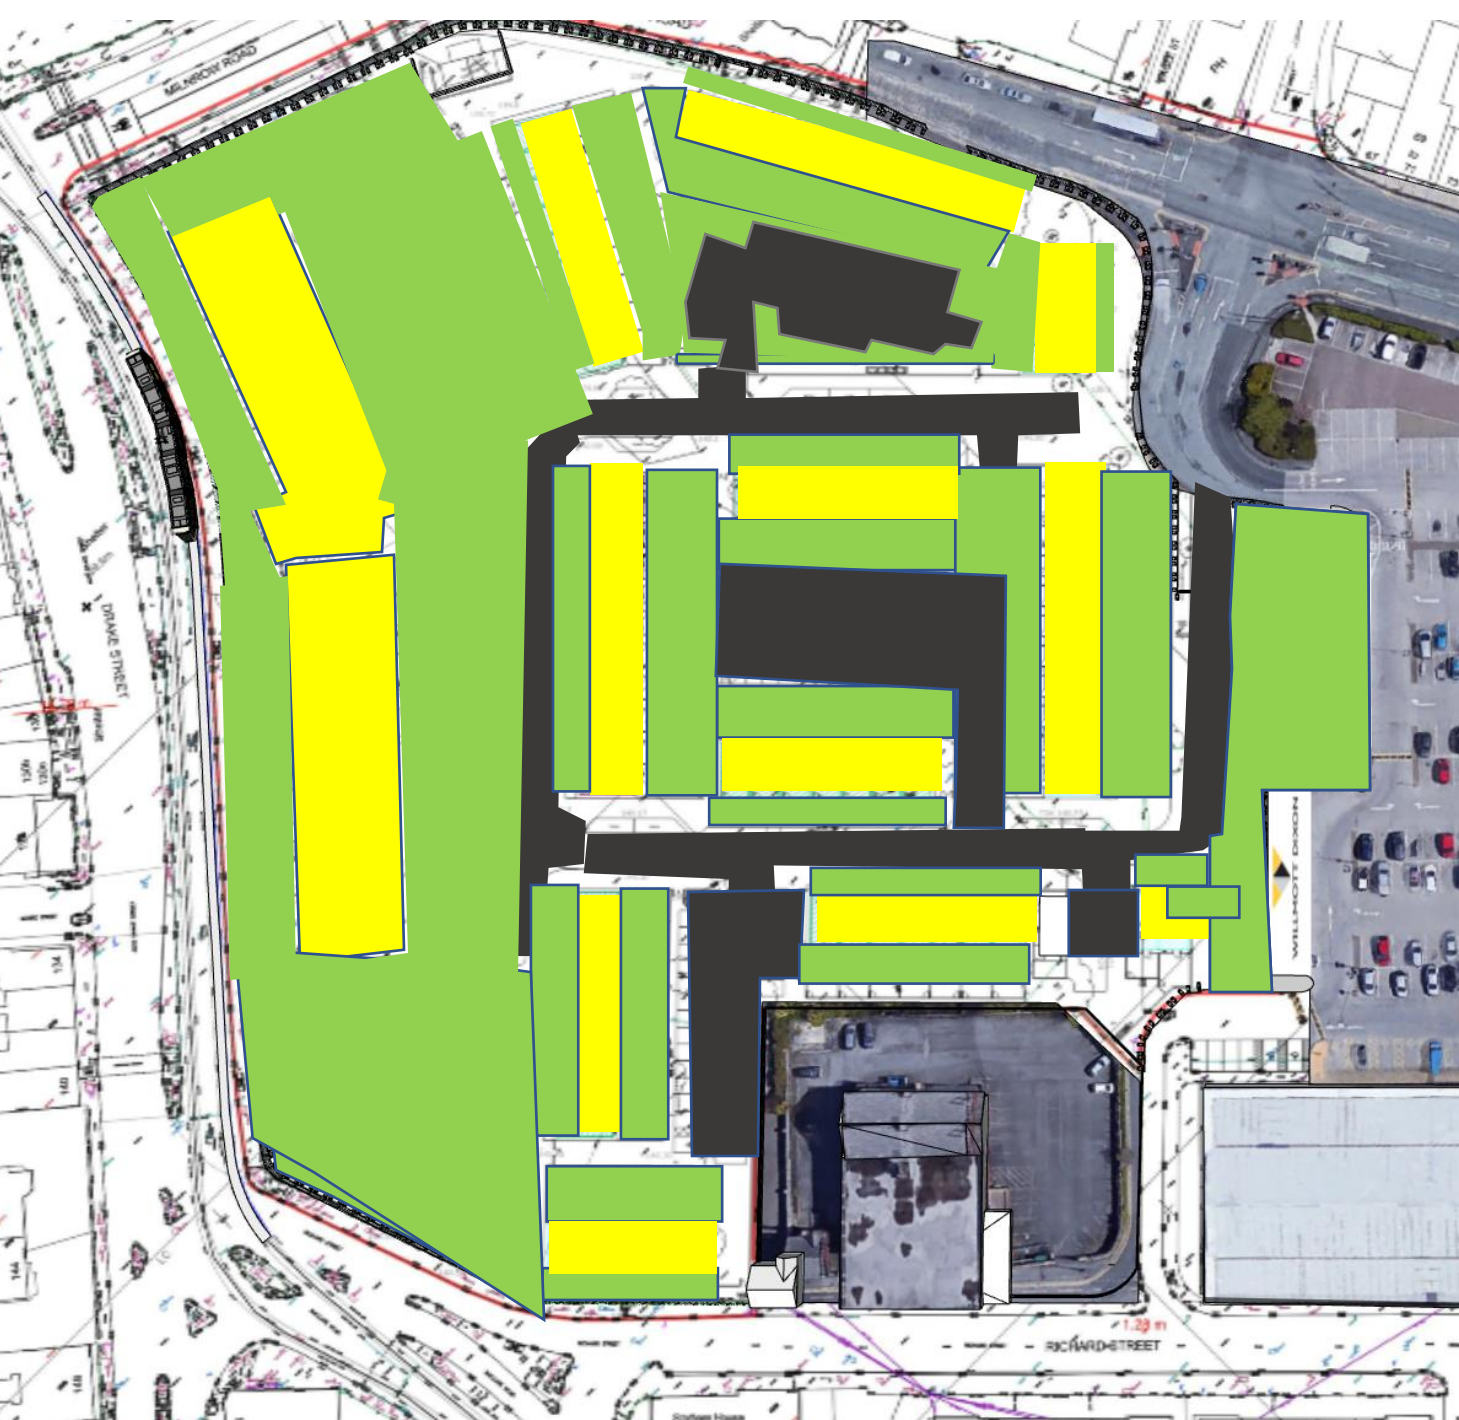

Week 111-116



External Works



Units complete



Tarmac/White line / clean
