


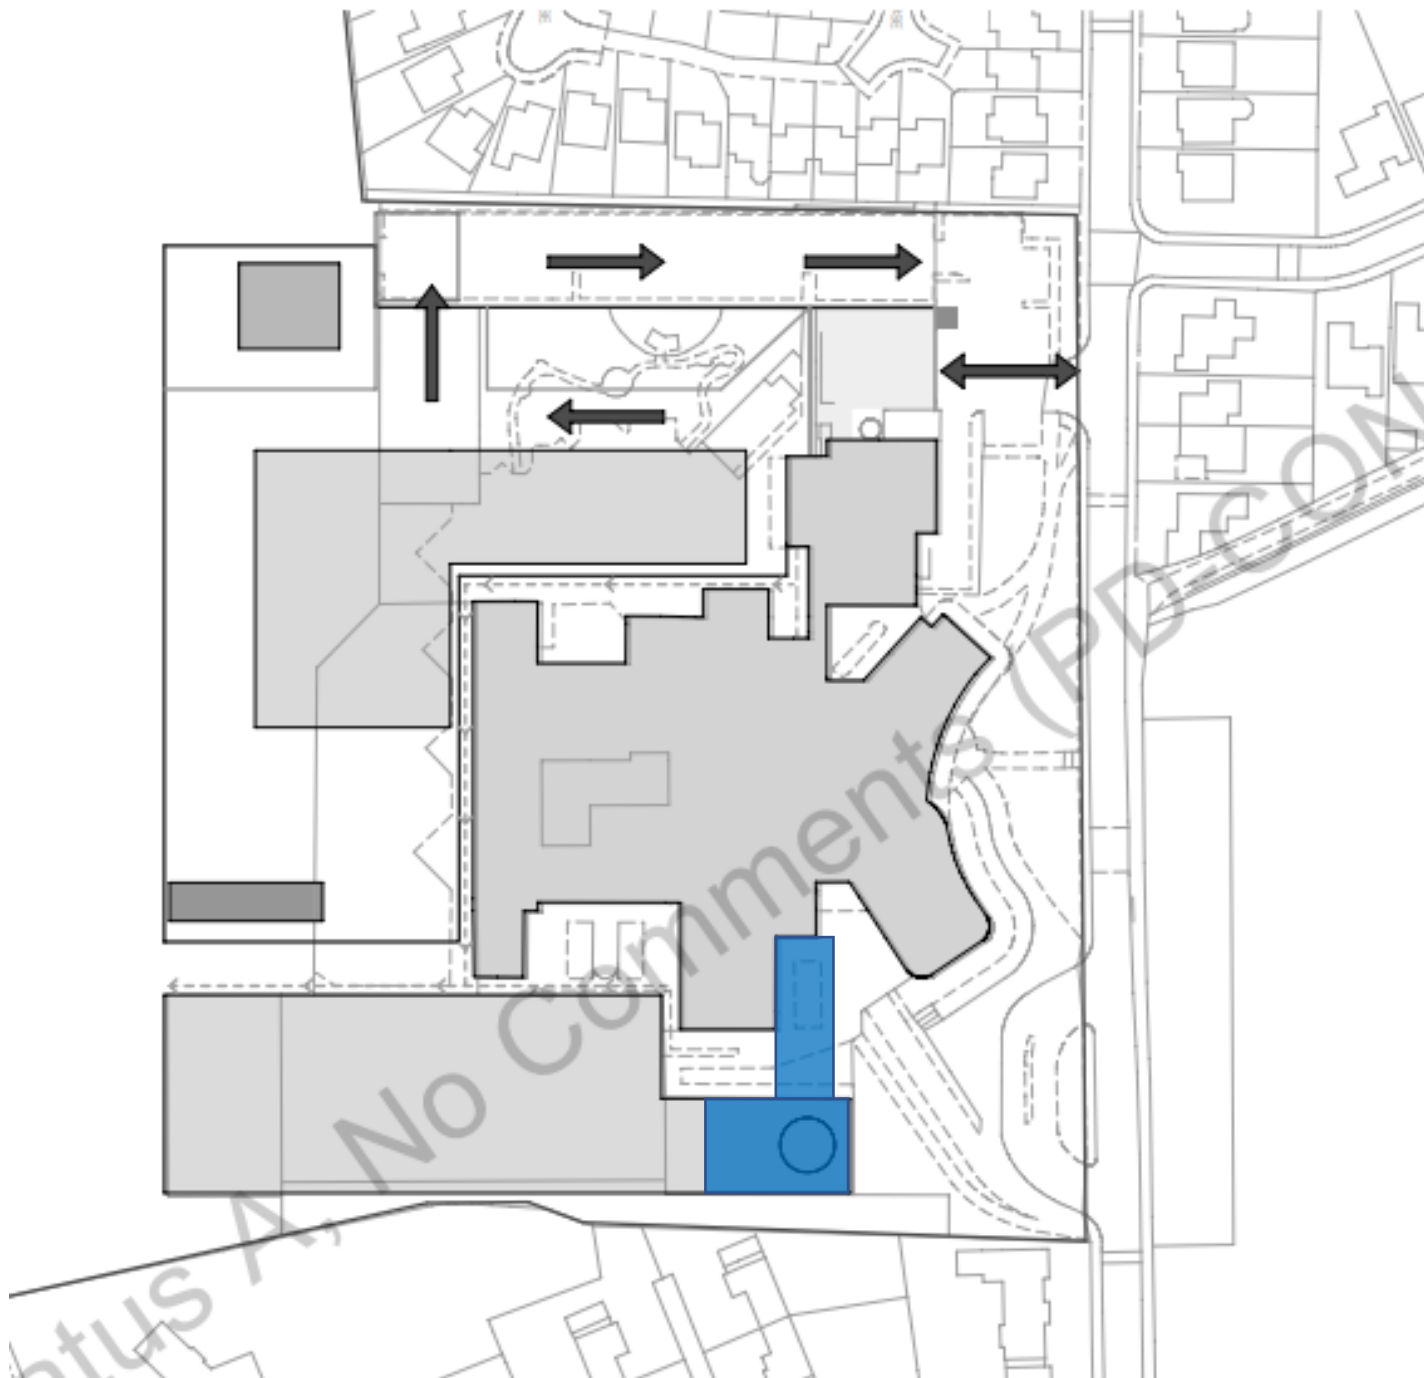


Section 1 – Work Areas

Possession Date: 27.03.23

Completion Date: 17.04.23

To the south of the site the following works will be carried out:

- Install foundations for the temporary dining canopy
- Install kitchen container unit
- Install temporary dining canopy
- Install services to the temporary kitchen.

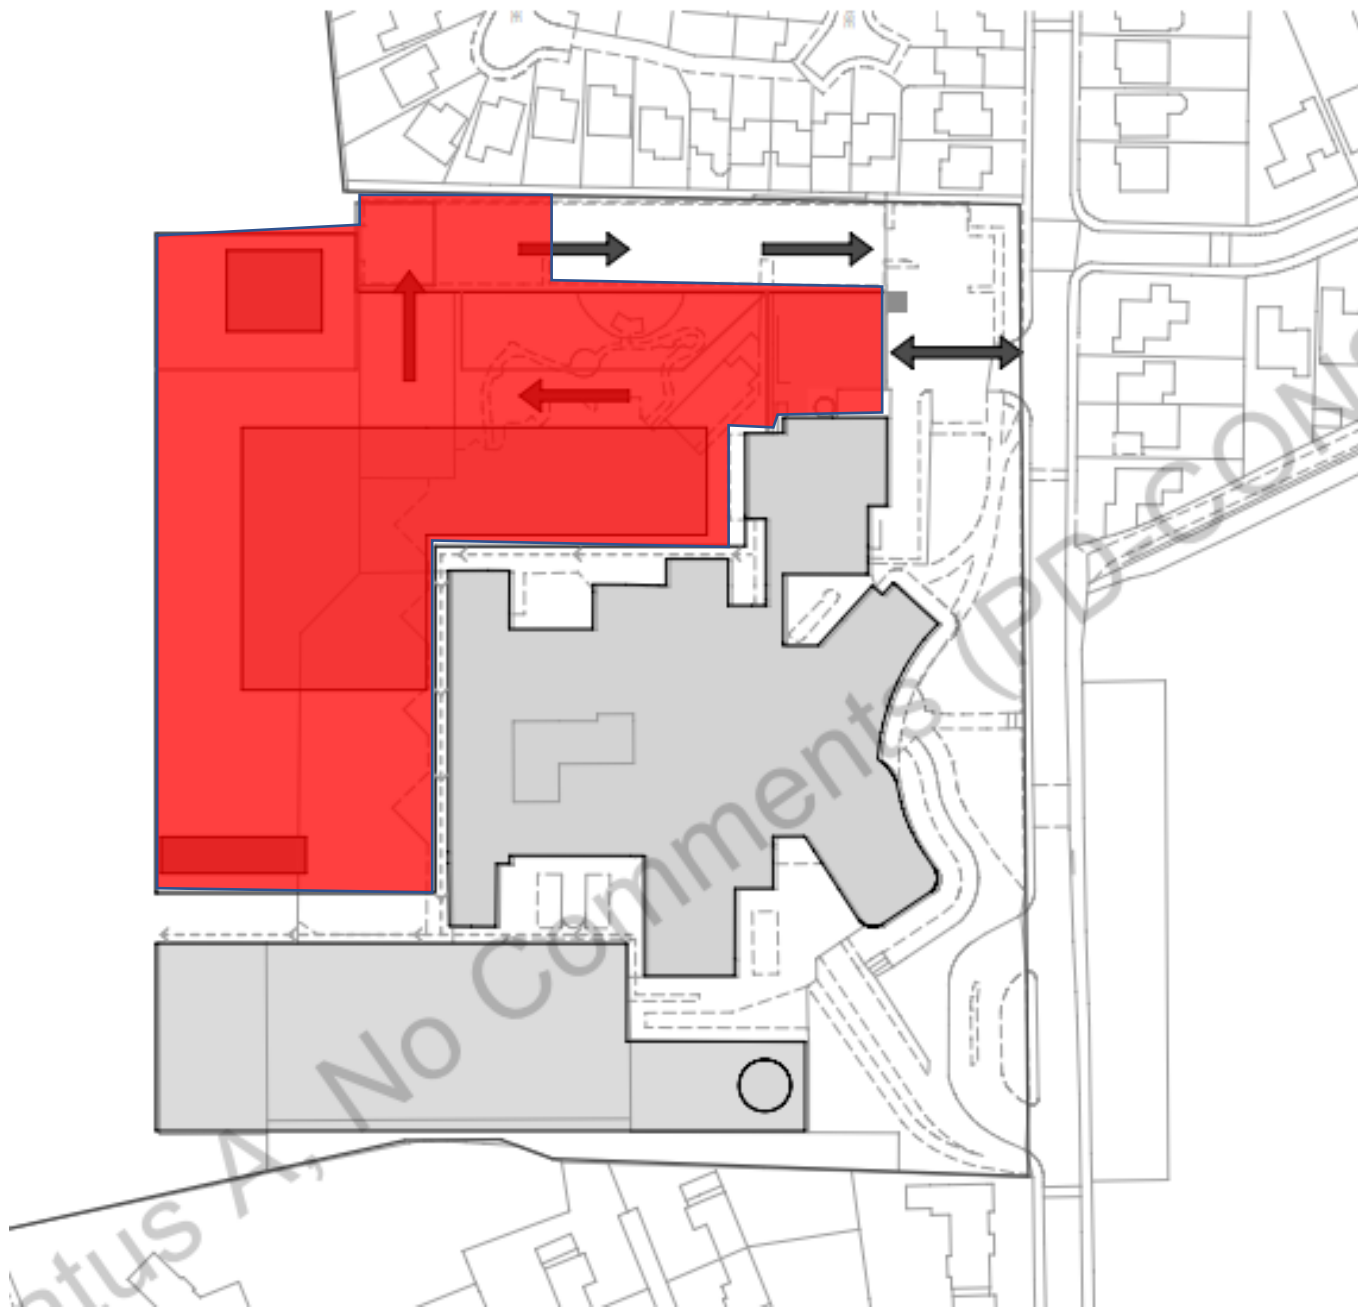

Section 2 – Work Areas




Possession Date: 13.03.23

Completion Date: 02.09.24

Works include the following:

Construction of the new school building and substation including associated external works

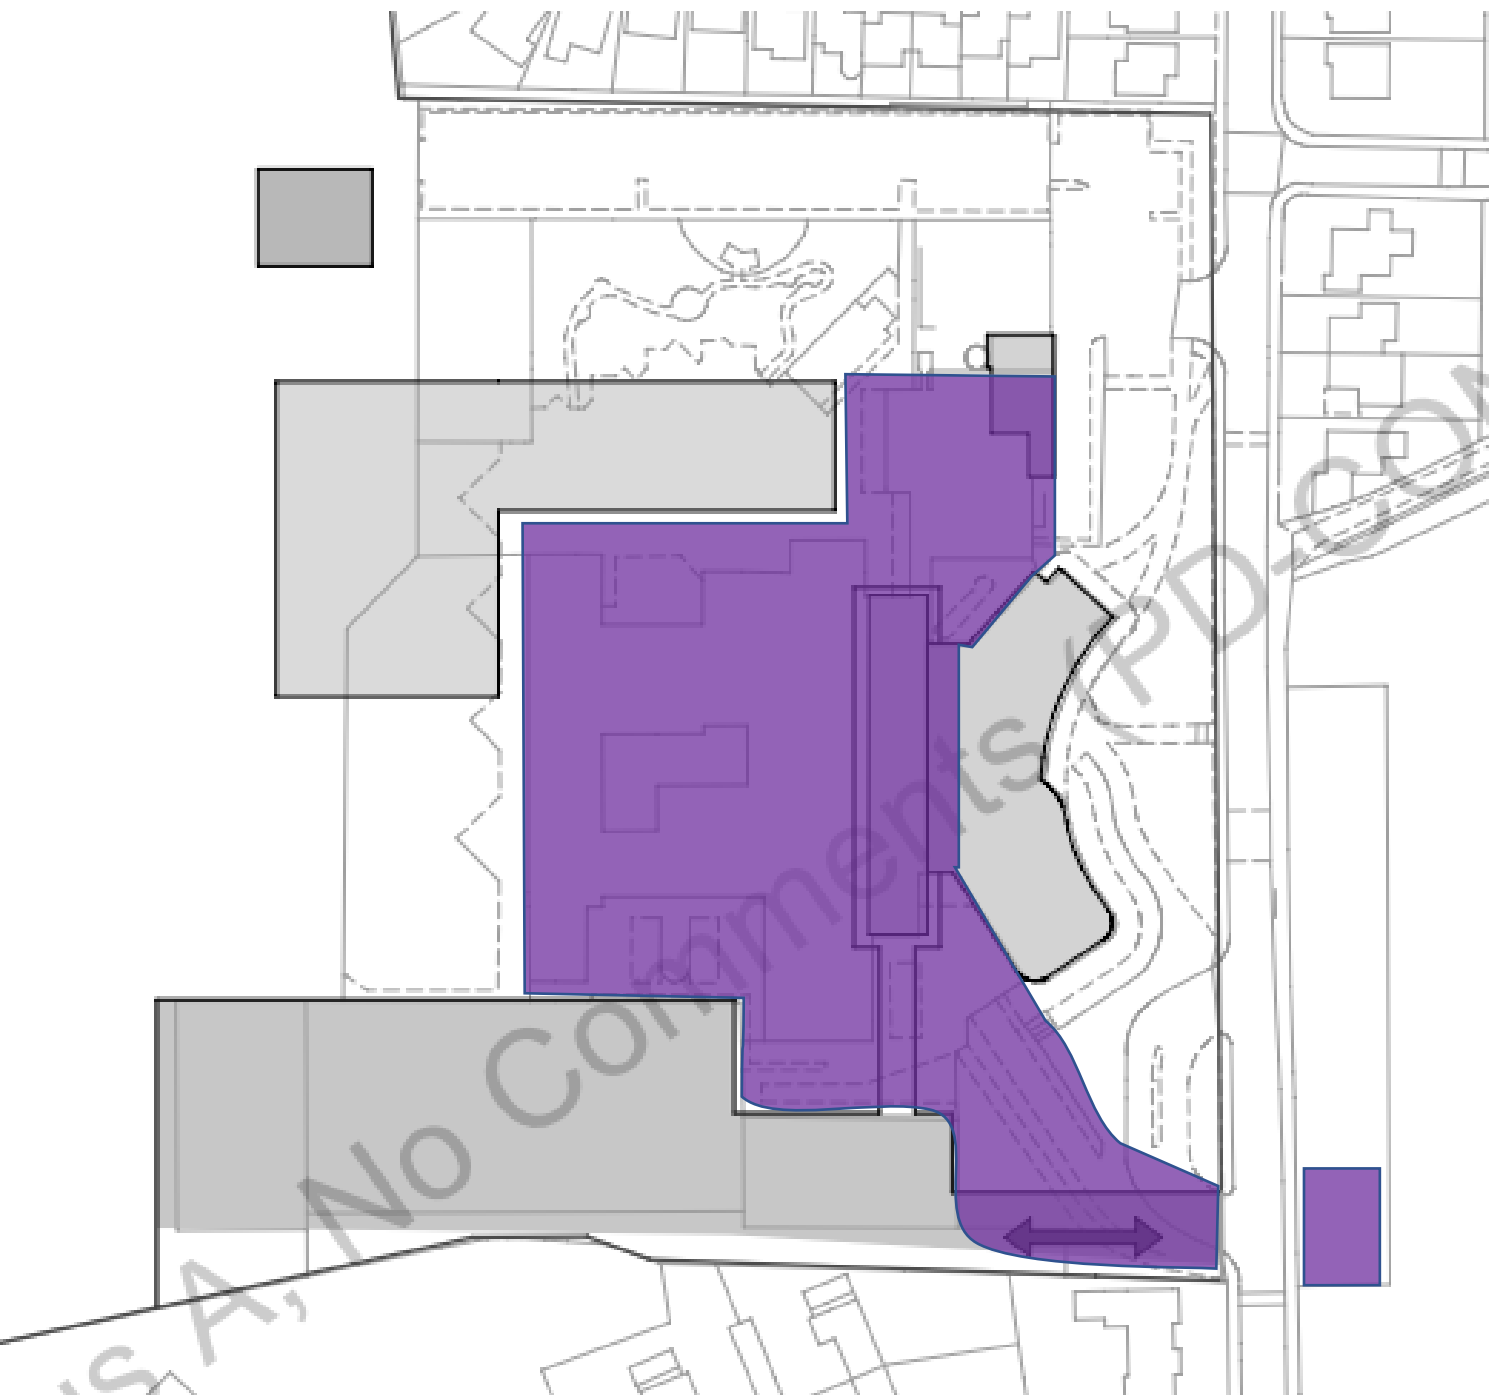


Section 4 – Work Areas

Possession Date: 03.09.24

Completion Date: 09.06.25

Works include the following:

- Alteration of hoarding line.
- Asbestos surveys and removal
- Demolition and external works

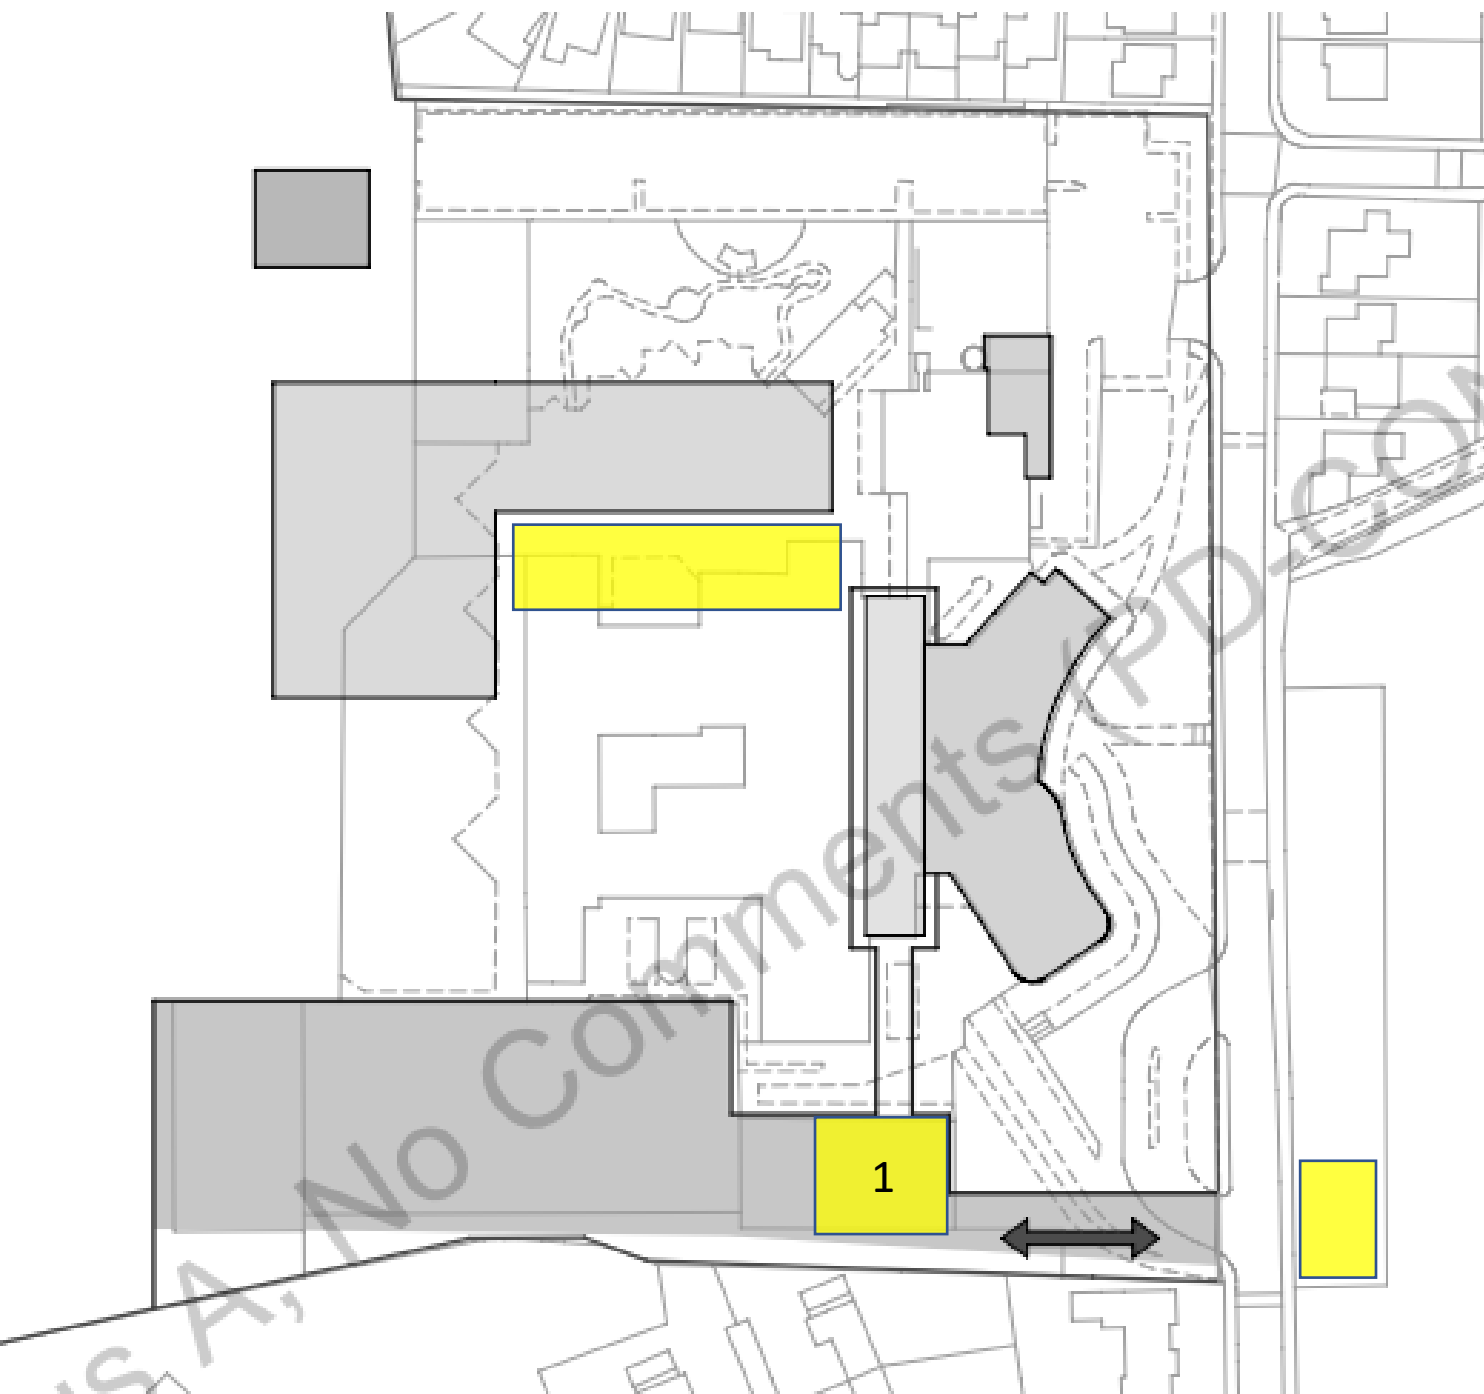

Section 5 – Work Areas


Possession Date: 03.09.24

Completion Date: 12.02.25

Works include the following:

- External dining area canopy and associated external works.
- Moving the kitchen unit into its permanent location

NOTE: Area 1 - Moving the kitchen unit will take one day, timing to be agreed with the school

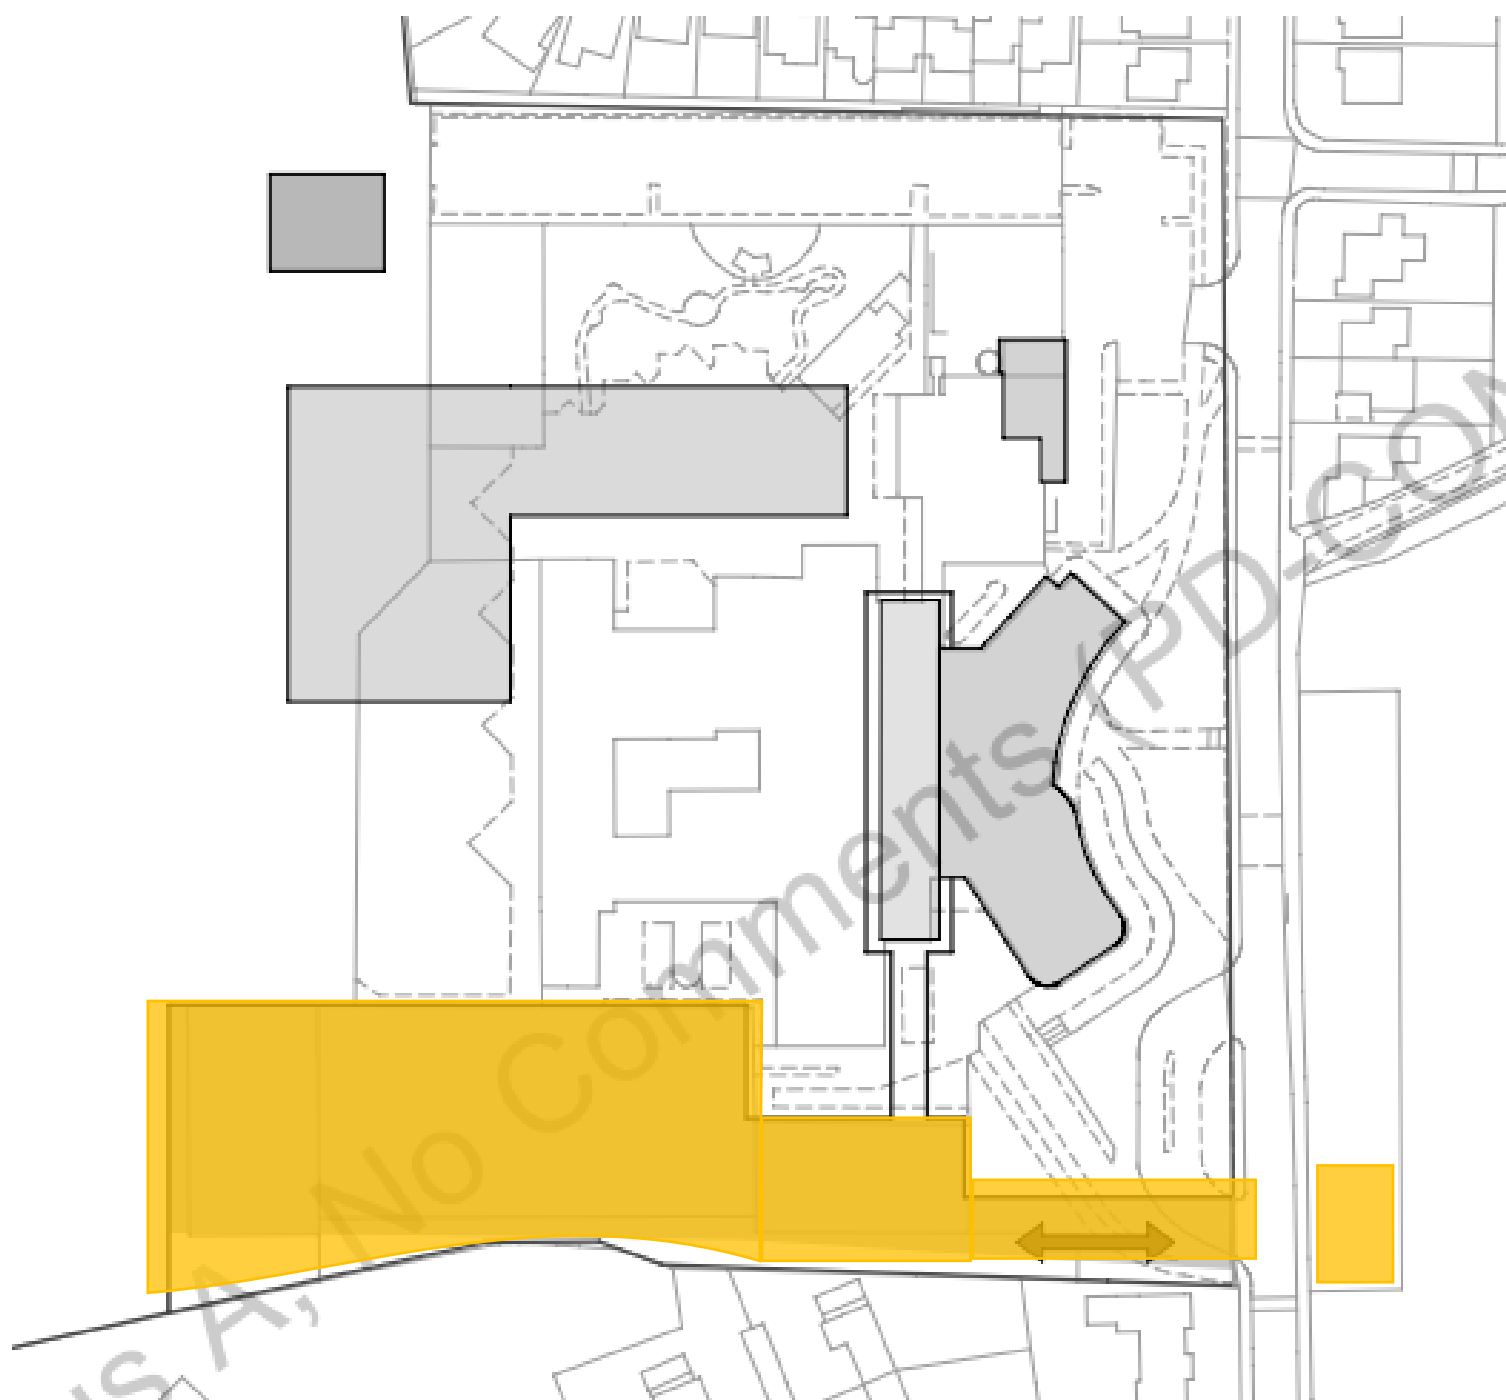

Section 6 – Work Areas

Possession Date: 12.02.25

Completion Date: 09.06.25

Works include the following:

- Removal of MUGA and installation of playing field in the same location
- Resurfacing of existing MUGA pitches
