

Week 5 – W/E 13.09.2024 – Stonework dismantling and window repairs



Crane used to dismantle upper stonework of entrance from the entrance gable and oriel window




Stonework dismantled from the entrance gable



All stonework referenced and identified on a reference drawing before dismantling



Roof cowel removed for repair

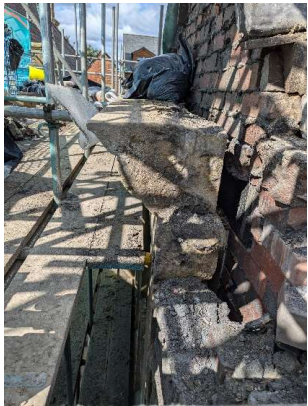

Gable dismantled down to the window head detail and temporary support provided




Displaced pilaster stone during dismantling.



First repaired windows re-installed



Repaired kitchen window re-installed

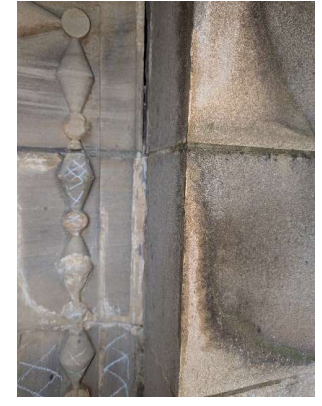

Indent repairs agreed on site. Some further dressing back agreed.
